

# CHARLES L. GIDEON ELEMENTARY SCHOOL

Weekly Construction Progress Report  
Week 11/12/18-11/16/18



The Kindezi School

**Balfour Beatty**

# 11/5/18-11/10/18 Activities



The Kindezi School

- Poured foundations
- Completed forming wall - pour wall Friday (11/9)
- Completed install of grease lines
- Started MEP underground rough at Kitchen
- Interior framing and MEP at renovation
- GP removed overhead power to Gym
- Saturday (11/10) work - Due to rain events this week



Complete Retaining Wall Formwork



Underground Plumbing Rough



Continuous Footing

**Balfour Beatty**


# 11/5/18-11/10/18 Activities Continued



The Kindezi School



Sawcut Slabs to Install Plumbing

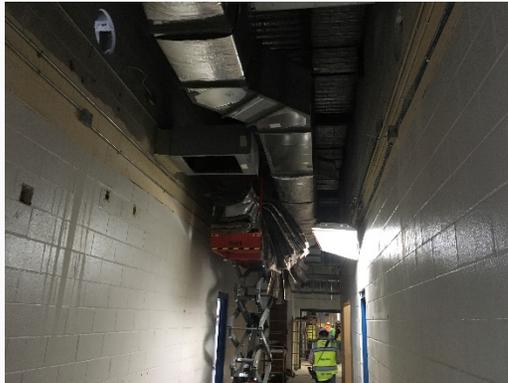

Insulating Duct



Drywall/Framing & MEP Rough

**Balfour Beatty**

# 11/12/18-11/16/18 Activities


- Excessive rain shut down exterior activities
- Stripped forms from cast in place wall
- Interior framing and MEP at renovation



The Kindezi School



Interior renovation MEP rough and framing / drywall

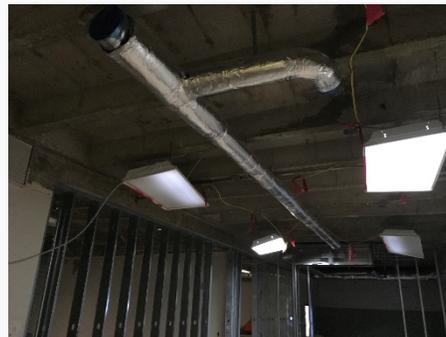

**Balfour Beatty**

# November Aerial Pictures



The Kindezi School



**Balfour Beatty**  
Construction

Gideons Elementary School

Print #181111077  
Date: 11/11/18  
Lat/Lon: 33.730688 -84.405279  
Order No. 65099  
Aerial Photography, Inc. 954-968-0484



**Balfour Beatty**  
Construction

Gideons Elementary School

Print #181111078  
Date: 11/11/18  
Lat/Lon: 33.730688 -84.405279  
Order No. 65099  
Aerial Photography, Inc. 954-968-0484

**Balfour Beatty**



## 11/19/18-11/23/18 Activities

- Renovation drywall, sprinkler, in wall inspections
- FW and DW site utilities
- Complete foundations and Kitchen slab rough
- Complete curb and gutter
- Waterproofing of retaining wall
- Roofing remobilization for renovation white cap
- Closed for Thanksgiving Holiday

## Project Schedule

- Project schedule impacted by delayed LDP and Building Permit procurement
- Project substantial completion: 8/29/19 per 11/6/18 schedule update

## Project Financials

- Current contract value: \$14,400.00
- Approved OCO 1 \$75,856.45 – Pending execution

**Balfour Beatty**
