

EMMA HUTCHINSON ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 4/13/20-4/17/20



Goodwyn, Mills, & Cawood

Balfour Beatty

Current Activities 4/13/20 - 4/17/20

- Begin install of copings on roof at building 2010
- Continue roof demo and replacement at building 2021
- Pour loading dock ramp
- Begin form and pour of ADA ramp and sidewalks
- Begin install of curtain wall system at entry
- Complete tile in restrooms at building 2010
- Complete epoxy floors in restrooms at 2010
- Begin install of markerboards and tackboards at building 2020 & 2021
- Begin install of toilet fixtures in restrooms at building 2020 & 2021
- Install water fountains at building 2021

Upcoming Activities 4/20/20 – 4/24/20

- Continue demo and reapplication of roofing at building 2021 & 2020
- Continue form and pour sidewalks and ADA ramp
- Continue install of exterior curtain wall system
- Begin install of ceiling tile at building 2010 and in Cafeteria
- Begin install of toilet partitions at building 2021
- Begin install of Millwork at building 2021
- Begin install of doors at building 2021



Begin Install of Curtain Wall System at Entry




Begin Form and Pour of ADA ramp and Sidewalks

Activities



Install Markerboards and Tack Boards at Building 2020 & 2021

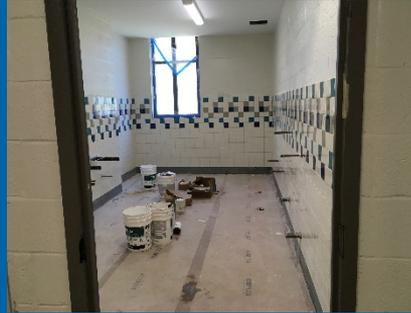

Complete Tile and Epoxy Floors at Building 2010 Restrooms



Install Toilet Fixtures in Restrooms at Building 2021

GMC

Goodwyn, Mills, & Cawood



Pour Loading Dock Ramp



Continue Roof Demo and Replacement at Building 2021



Begin Install of Copings on Roof at Building 2010

Balfour Beatty

Project Schedule

- Project Substantial Completion: June 2020 per 04/07/2020 schedule update
- Schedule Status: On Schedule



Project Financials

- Construction Budget: \$7,680,000
- Progress Billed to Date: \$4,085,607
- Budget Status: Within GMP



Goodwyn, Mills, & Cawood
