

JACKSON

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 10/02/2023-10/06/2023



Balfour Beatty

Current Activities 10/02/2023-10/06/2023

- Complete
 - Demo of block wall(s) upper level
- Started/Ongoing
 - Electrical safe-off
 - Temp. Lighting
 - Demo of hard ceilings upper level
 - Demo VCT and Ceiling Tiles lower level
 - Abatement ongoing at carpeted rooms
 - BBC Pending Pricing Revision 7 Drawings

Upcoming Activities 10/09/23-10/13/23


- Demolition of plumbing
- Demolition of casework
- Demo of HVAC and reloop waterpiping



Demolition ongoing
Electrical Safe-off ongoing



Progress Photos

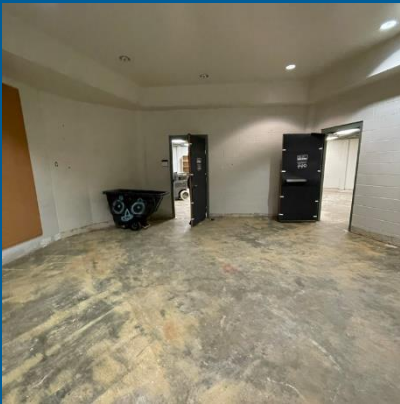

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$12,330,741.00
- Progress Billed to Date: \$793,135.38
- Budget Status: Within GMP

