

# JACKSON

## ELEMENTARY SCHOOL

*Weekly Construction Progress Report*  
*Week 10/09/2023-10/13/2023*



**Balfour Beatty**

## Current Activities 10/09/2023-10/13/2023

- Complete
  - Demo ceiling tiles lower level
  - Abatement complete at carpeted rooms
  - Plumbing disconnected
- Started/Ongoing
  - Electrical safe-off
  - Temp. Lighting
  - HVAC demo upper level
  - Demo of hard ceilings upper level
  - Abatement ongoing at plumbing lines
  - BBC Pricing Revision 7 Drawings

## Upcoming Activities 10/16/23-10/20/23


- Demolition of casework
- Demo of HVAC and reloop waterpiping



**Demolition ongoing  
HVAC Demo ongoing**



# Progress Photos

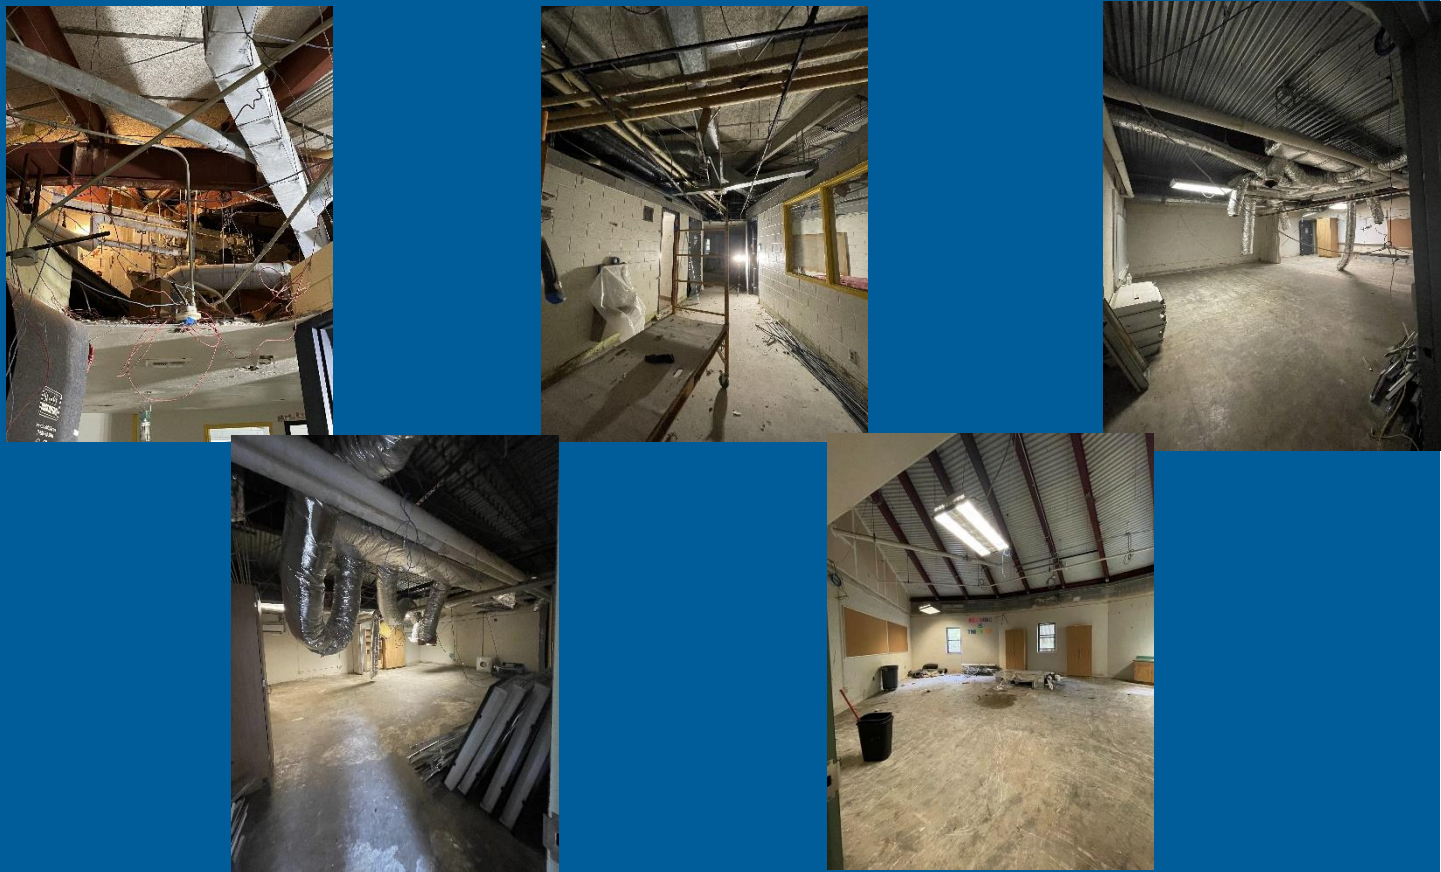

## Project Schedule

- Schedule Status: On Schedule



## Project Financials

- Construction GMP: \$12,330,741.00
- Progress Billed to Date: \$793,135.38
- Budget Status: Within GMP

