


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit center

WEEK ENDING 11/17/2023

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	07/31/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

PROJECT OVERVIEW

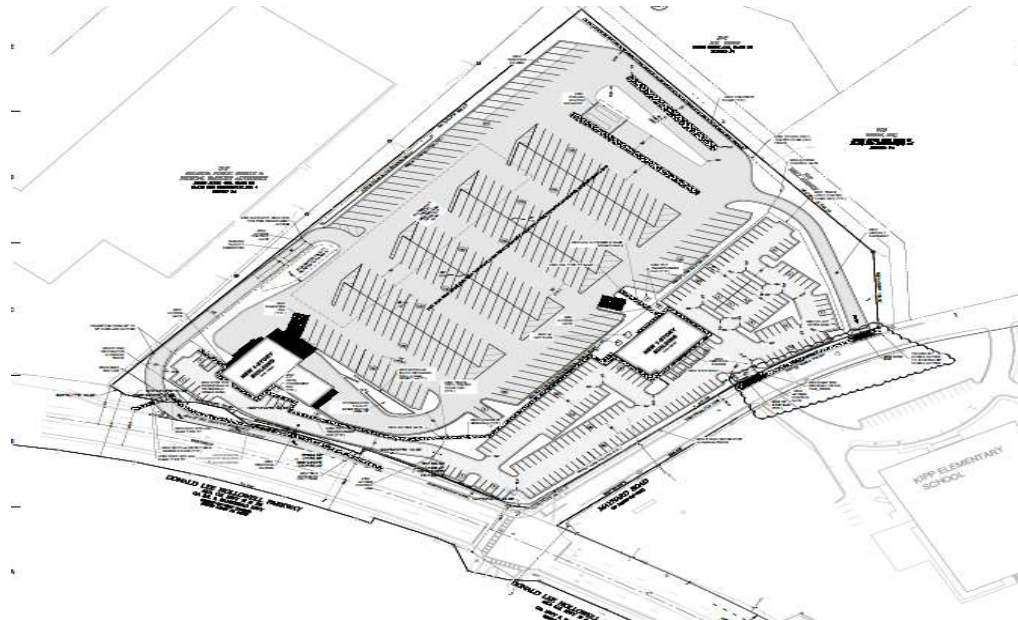

Construction Activities this week

- IN THE PROCESS OF CONDUCTING CIVIL WORK
- INSTALLING STORM STRUCTURES (MANHOLE 19-20) WHICH IS A 52 FT RUN. MANHOLE 23 SET AS WELL.
- COORDINATING A LOGISTICS PLAN FOR SS BORE ACROSS MAYNARD STREET
- EXCAVATING THE RETENTION BASIN.

CONSTRUCTION ACTIVITIES PLANNED (5 WEEK LOOK AHEAD)

THIS IS DEPENDENT UPON BUILDING PERMIT STATUS AND WEATHER.

- CONCRETE, REBAR, PLUMBING & ELECTRICAL EQUIPMENT DELIVERIES
- STRUCTURAL FOUNDATION LAYOUT
- CONTINUE TO WORK ON BUILDING PADS
- UNDERSLAB PLUMBING INSTALLATION (MEP INSTALLATION)
- CONCRETE WORK/POUR SLABS

MANPOWER LOG (WEEK OF 11/10/23)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	25	25	20	25	20

WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT

