


Construction Joke of the Week: What did the window glazier say when he cut himself on the window glass? - "This is extremely paneful!"

Project: CW Hill Elementary and Middle School **Week Ending: March 7, 2024**

THIS WEEK:

- Continued painting walls on level 1
- Continued hanging drywall for restroom ceilings on level 1 restroom
- Continued framing ceilings on level 1 and 2
- Continued fire sprinkler rough-in and dropping heads on level 1
- Continued fire alarm rough-in on level 1
- Continued intercom rough-in on level 1 and level 2
- Set UDS
- Set Generator
- Continued electrical rough-in and wiring panels on level 1
- Continued installing piping in AHU 101 on level 1
- Continued installing grilles and adjusting grilles on level 2
- Installed the retaining wall and pad for the transformer

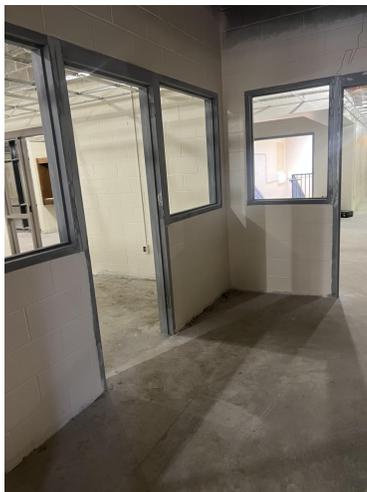

Window frames installation and painting in the security vestibule on level 2.



Installing ceiling grid and fire sprinkler rough-in on level 2.



Painting in the restrooms on level 1.



Installing the retaining wall and pad for the transformer

NEXT WEEK – March 10th - March 14th

- Install Interior lighting on level 1 and 2
- Continue painting walls on level 1
- Continue hanging drywall for restroom ceilings on level 1 restroom
- Continue framing ceilings on level 1 and 2
- Continue fire sprinkler rough-in and dropping heads on level 1
- Continue fire alarm rough-in on level 1
- Continue intercom rough-in on level 1 and level 2
- Continue electrical rough-in and wiring panels on level 1
- Continue installing piping in AHU 101 on level 1
- Continue installing grilles and adjusting grilles on level 2

Final Completion

- June 30, 2025

PREPARED BY:

Orisamola Richardson, Carroll Daniel Construction Co.
