


*Quote of the week: "Before anything else, preparation is the key to success."*

### Project: FL Stanton ES Renovation and Addition

**Week ending: June 14, 2024**

- Bore for new transformer relocation
- Fire pump install is complete
- Install acoustical panels in the gym
- Wall mat and scoreboard installation is complete
- Flooring of the administration area and the classroom portion
- Installed floor grate on top floor
- Complete finish seat wall

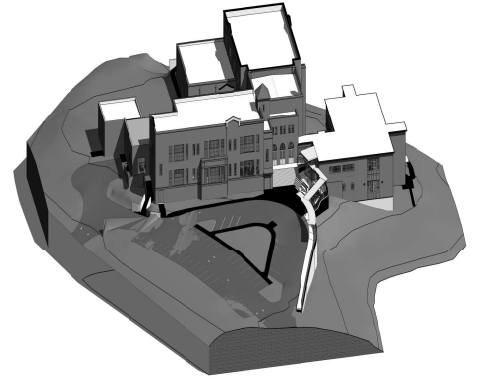


*Exterior window install is 70% complete*



*Sound absorbing wall panel and wall pads installation complete*



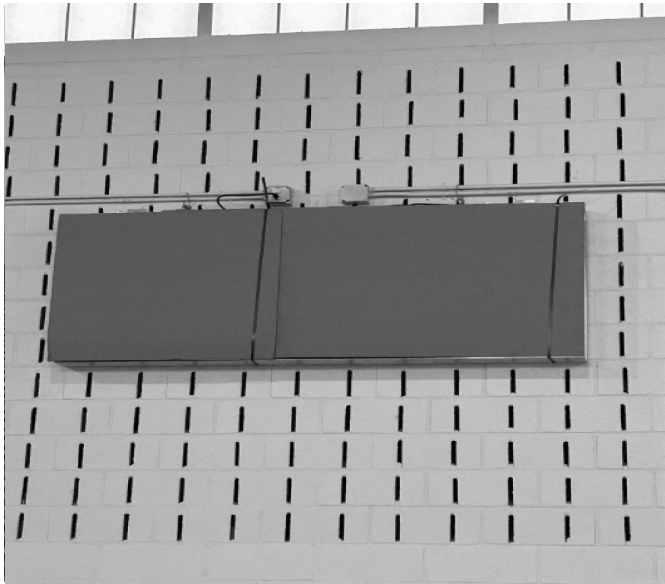

*Scoreboards install is complete*



*Continue with classroom VCT and casework install throughout*

## **NEXT WEEK – June 17 - June 21**

- Begin relocating transformer
- Install UDS and go hot on electrical
- Complete LVT and VCT install throughout
- Mechanical start-up to begin
- Continue with exterior paint
- Complete exterior window install
- Complete electrical and mechanical trim out
- Continue with final clean

## **SCHEDULED DATE OF SUBSTANTIAL COMPLETION**

- June 30 , 2024

## **Final Completion**

- June 30, 2024

## **PREPARED BY:**

Jahaziel Lee, Carroll Daniel Construction Co.

