


Quote of the week: "Be humble. Be hungry. And always be the hardest worker in the room."

Project: FL Stanton ES Renovation and Addition

Week ending: May 10, 2024

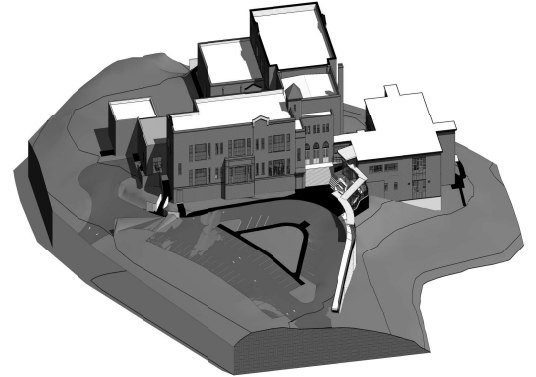

- Continue with gym equipment install
- Begin laying brick at the security vestibule
- Begin sidewalk forming and pour back
- Continue with interior painting on level 1 and Gym area
- Exterior windows have been delivered
- Front entrance stair pour back is complete
- Continue with ceiling grid install throughout



Formed and poured sidewalk at playground area



Continue with ceiling tile install



Continue with resinous flooring work



Monument sign complete, and currently ready for LED boards.

NEXT WEEK – May 13 - May 17

- Continue with sidewalk forming and pour back
- Complete ceiling grid install
- Begin ceiling cover up inspections
- Begin installing exterior windows
- Continue with gym equipment install
- Begin installing access panels
- Begin canopy block-out install
- Complete resinous flooring

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- June 30 , 2024

Final Completion

- June 30, 2024

PREPARED BY:

Jahaziel Lee, Carroll Daniel Construction Co.

