

**Quote's of the Week:** "Change your thoughts and you change your world"- Norman Vicent  
"The best preparation for tomorrow is doing you best today" — H. Jackson Brown, Jr.

## Project: Hank Aaron Academy Additions & Modifications


Week Ending: February 28, 2025

### THIS WEEK:

- Footing work is 90% complete
- Foundation wall pouring is completed
- MEP rough-in work continues in the cafeteria area
- Backfilling has begun
- Installation of CMU foundation walls has begun
- Underground plumbing work has started



*Installing CMU foundation wall*

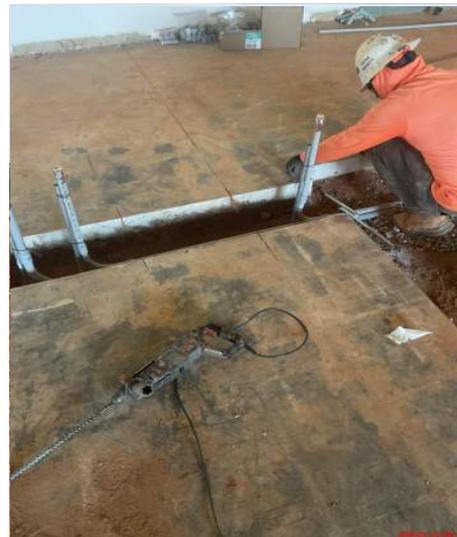

*Electrical rough-in in cafeteria*



*Foundation wall complete*



*Backfilling in progress*

## **NEXT WEEK – March 3 - March 7**

- Continue backfilling
- Complete underground plumbing
- Begin underground electrical work
- Start laying wall in the cafeteria
- Continue MEP rough-in work in the cafeteria

## **SCHEDULED DATE OF SUBSTANTIAL COMPLETION**

- December 1, 2025

## **PREPARED BY:**

Karee Shaw, Carroll Daniel Construction Co.

