

Quote of the Week: "It is our attitude at the beginning of a difficult task which, more than anything else, will affect its successful outcome." — William James

Project: Hank Aaron Academy Additions & Modifications


Week Ending: May 30, 2025

THIS WEEK:

- Weather delay: 4 days
- Began installation of low roof
- Ongoing installation of split face block around perimeter and Plainstone CMU at pilasters
- Continuing MEP rough-in
- Ongoing installation of interior CMU walls in low roof area
- Initiated kitchen demo



Installing Low Roof

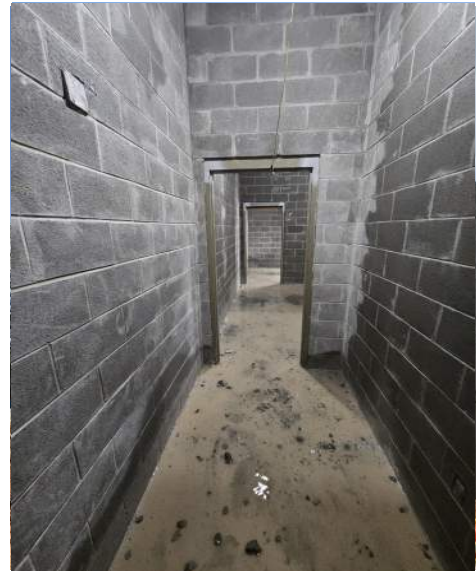

Interior CMU Wall at low roof



Waterproofing & Split Face Block Installation at Perimeter



MEP Overhead Rough- In

NEXT WEEK – June 2 - June 5

- Complete low roof installation
- Complete waterproofing
- Complete Plainstone CMU at pilasters
- Continue MEP overhead rough-in
- Continue installing split face block around the perimeter
- Begin demolition of main entrance
- Start epoxy flooring installation in serving line

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- December 31, 2025

PREPARED BY:

Karee Shaw, Carroll Daniel Construction Co.


Hank Aaron - Weekly Progress Updates
Carroll Daniel Construction Company
