

Quote of the Week: "Do the best you can until you know better. Then when you know better, do better." - Maya Angelou

Project: Hank Aaron Academy Additions & Modifications

Week Ending: July 25, 2025

THIS WEEK:

- MEPF rough-in work is ongoing
- Block fill continues at gymnasium and low roof areas
- Framing ceiling in storage room
- Curb installation in progress at east façade parking lot
- Operable partition installed in cafeteria
- Ceiling grid installation started in classrooms
- Day 1 Scope of Work Completed



Day 1 Floating Canopy Installed




Day 1 Monument Sign Complete





Curb poured near Eastside of building

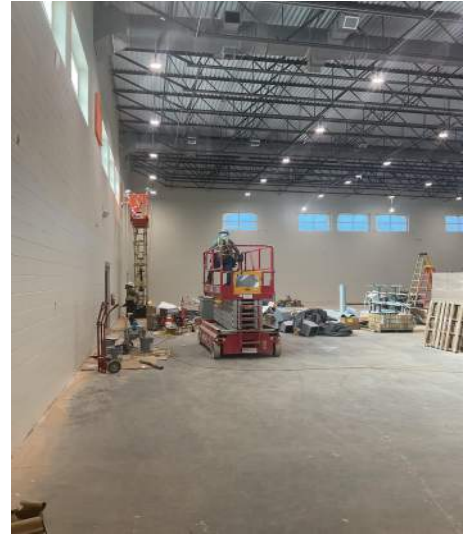

Block Fill in Gym

NEXT WEEK – July 28 - Aug 1

- Complete MEPF overhead rough-in
- Continue block fill at gym area
- Continue ceiling grid installation
- Begin dryfall painting in stage area

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- December 31, 2025

PREPARED BY:

Karee Shaw, Carroll Daniel Construction Co.

