

***Joke of the Week:** What are plumber's least favorite vegetables? Leeks*

Project: Hank Aaron Academy Additions & Modifications

Week Ending: August 22, 2025

THIS WEEK:


- Painting on bump-outs and stage area completed
- Epoxy floors in locker rooms and bathrooms completed
- Ceiling grid framing 97% complete
- Coping installation started
- Wall tile installation started
- Lighting 98% complete
- Epoxy flooring completed
- Ceiling cover inspection in low roof area passed



Curbs and paving completed



Painting on bump-outs complete

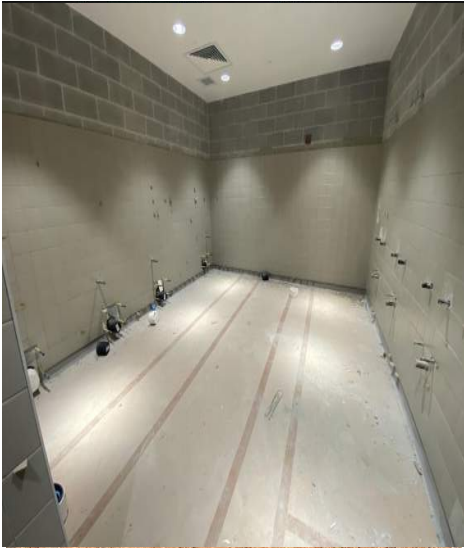

Wall Tile



Stage area painting completed



Exterior lighting



Ceiling Grid





Exterior View



East side exterior view

NEXT WEEK – Aug 25 - Aug 29

- Continue tile installation
- Complete coping Installation
- Continue wall tile installation
- Continue MEP Trim work
- Install basketball goals

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- December 31, 2025

PREPARED BY:

Karee Shaw, Carroll Daniel Construction Co.

