

Quote of the Week: *"I'd rather regret the things I've done than regret the things I haven't done."* —Lucille Ball

Project: Hank Aaron Academy Additions & Modifications

Week Ending: July 31, 2025

THIS WEEK:

- MEPF rough-in work ongoing above stage area
- Blockfill continues in gymnasium and low roof areas
- Dryfall painting started in gymnasium
- Ceiling grid framing ongoing
- Sheetrock ceiling installation started
- Curb completed at east façade parking lot
- GAB laid at east façade parking lot
- Water heaters being installed



Exterior view of bus loop entrance.



Building exterior – front-facing view






Gym ceiling dryfall finished



Ceiling drywall installation



Blockfill completed in classroom

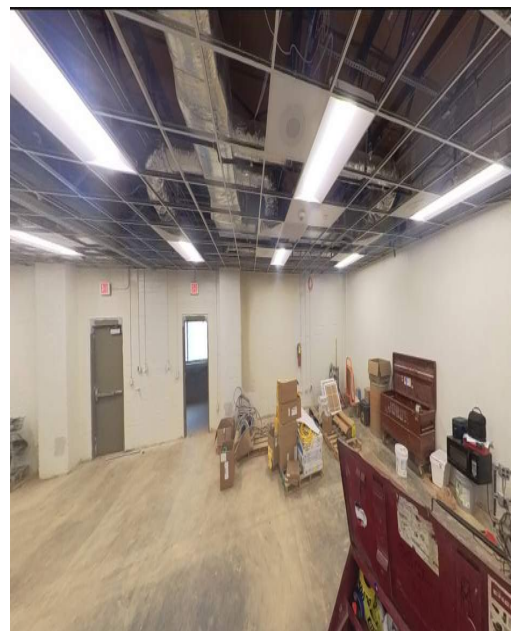

Entrance to cafeteria, view from gym





Rear exterior view of building



East side exterior view

NEXT WEEK – Aug 4 - Aug 8

- Continue MEPF overhead rough-in stage area
- Continue block fill in the low roof area
- Continue sheetrock ceiling installation
- Finish dryfall painting in the stage area

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- December 31, 2025

PREPARED BY:

Karee Shaw, Carroll Daniel Construction Co.

