

HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 2/1/19

This Week's Activities:

- 2nd Grade Pod – Frame Walls
- 2nd Grade Pod – Electrical Wall Rough In
- 2nd Grade Pod – Install Duct, Piping, & WSHP
- 2nd Grade Pod – In Wall Inspection
- Media Center – Interior Demolition
- Media Center – Core Drilling for Floor Rough In
- Media Center – Electrical Floor Rough In
- Media Center – Install Duct, Piping, & WSHP
- 1st Floor – Interior Demolition & Sawcut
- 1st Floor – Excavate for Grade Beams
- 3rd Grade Pod – Interior Demolition
- West Curtainwalls – Install Footings


Next Week's Activities:

- 2nd Grade Pod – Hang & Finish Drywall
- 2nd Grade Pod – Duct Seal Inspection
- 2nd Grade Pod – Insulate Duct & Piping
- 2nd Grade Pod – Paint Walls
- Media Center – Electrical Floor Rough In
- Media Center – Install Duct, Piping, & WSHP
- 1st Floor – Install Grade Beams
- 3rd Grade Pod – Interior Demolition
- West Curtainwalls – Frame & Pour Kneewalls

**HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE**

Week Ending 2/1/19

PROGRESS PHOTOS:

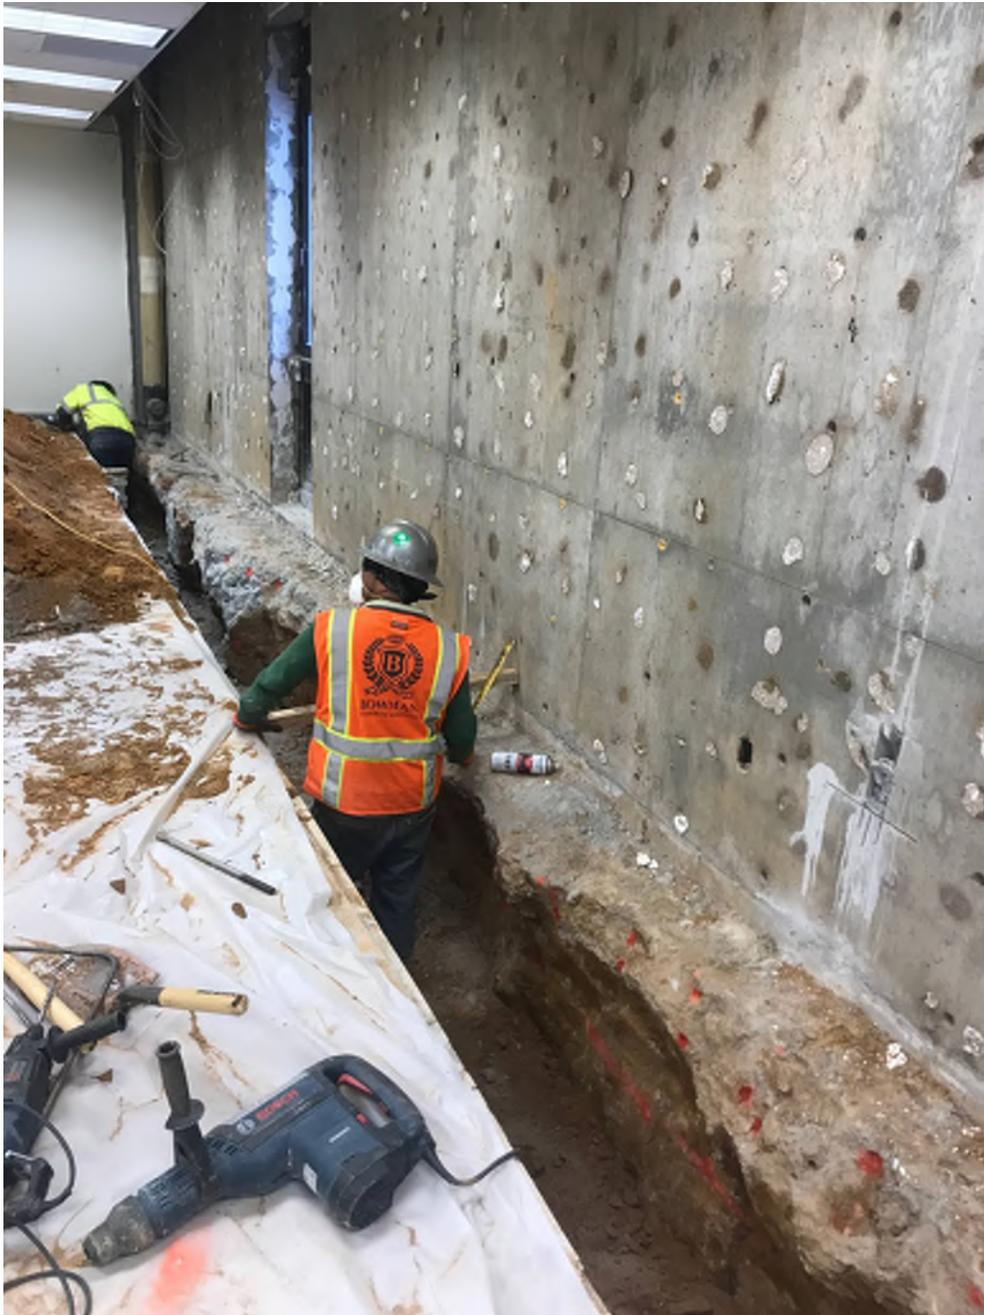

HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 2/1/19



HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 2/1/19



HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 2/1/19



HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 2/1/19





HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 2/1/19

SCHEDULE:

- Substantial Completion Date: June 30, 2019
- Schedule Status: On Schedule

BUDGET:

- Construction Budget: \$8,400,000
- Billed to Date: \$4,672,509.47 (Through 12/31/2018)
