

HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 2/8/19

This Week's Activities:

- 2nd Grade Pod – Frame Walls
- 2nd Grade Pod – Hang and Finish Drywall
- 1st Floor – Excavate for Grade Beams
- 1st Floor – Begin Installing Grade Beams
- 3rd Grade Pod – Interior Demolition
- 3rd Grade Pod – Frame Walls
- West Curtainwalls – Excavate for footings and knee walls
- Removing existing trees
- Installing new trees

Next Week's Activities:

- 2nd Grade Pod – Insulate Duct and Piping
- 2nd Grade Pod – Paint Walls
- 2nd Grade Pod – Install Storefronts
- 2nd Grade Pod – Install Ceiling Grid in Commons Area
- 1st Floor – Finish Installing Grade Beams
- 3rd Grade Pod – Electrical Wall Rough In
- 3rd Grade Pod – Install Duct, Piping, and WSHP
- 7th Grade Pod – Interior Demolition
- Art/Coding/Technology – Interior Demolition
- West Curtainwalls – Pour Footings
- West Curtainwalls – Frame and Pour Kneewalls

**HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE**

Week Ending 2/8/19

PROGRESS PHOTOS:




HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 2/8/19



HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 2/8/19



HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 2/8/19

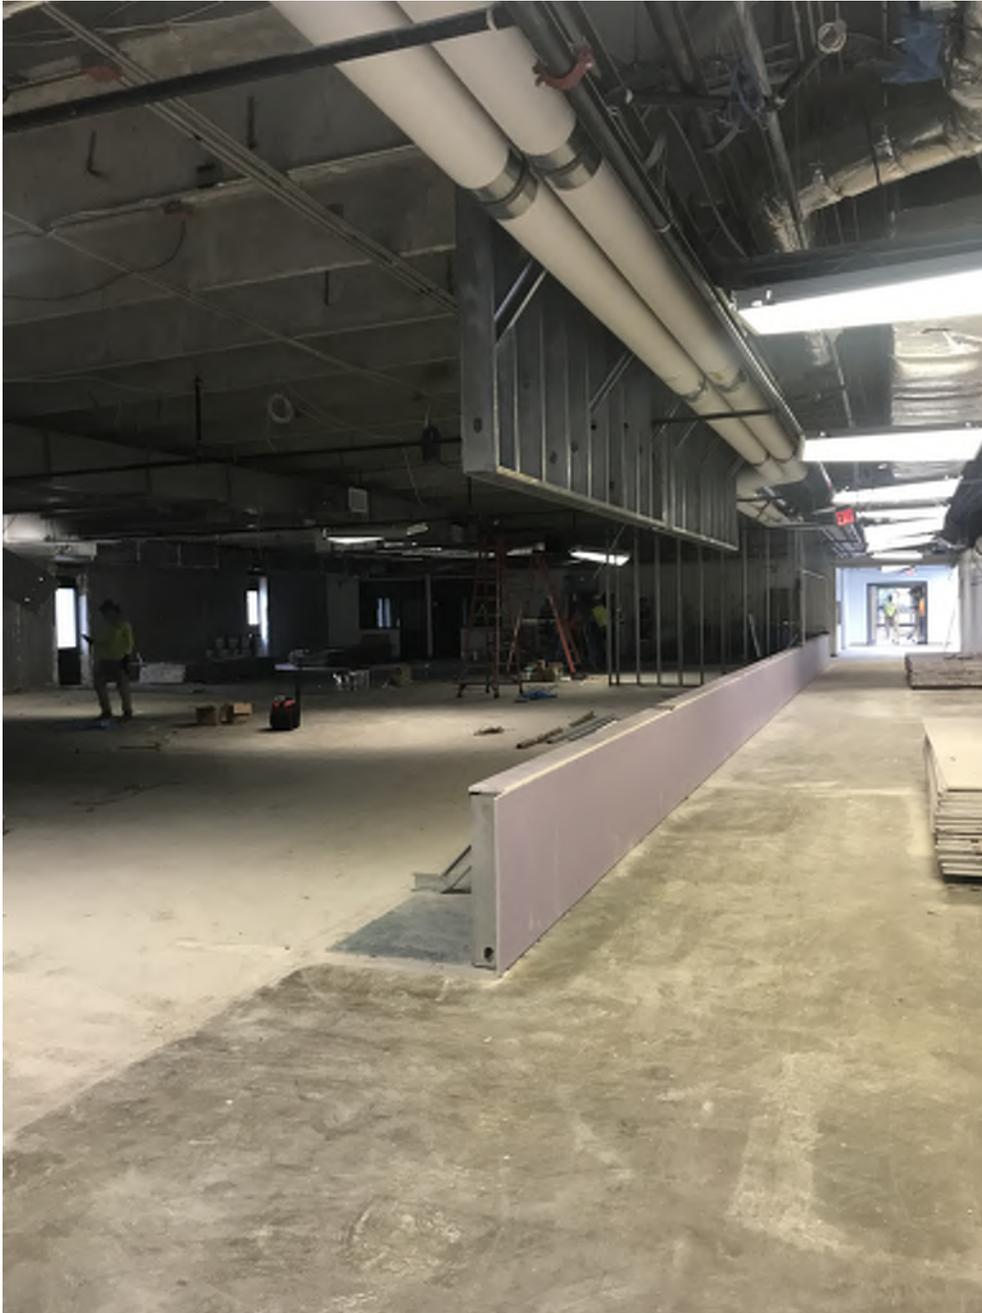

HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 2/8/19





HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 2/8/19

SCHEDULE:

- Substantial Completion Date: June 30, 2019
- Schedule Status: On Schedule

BUDGET:

- Construction Budget: \$8,400,000
- Billed to Date: \$4,845,049.47 (Through 1/31/2019)
