

HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 07/14/18

COMPLETED ACTIVITIES:

- Demolition of 5th Grade Pod
- Framing of 5th Grade Pod Walls
- Electrical Wall Rough-In in 5th Grade Pod
- Installation of Interior Storefronts in 5th Grade Pod
- Overhead MEP Rough-In in 5th Grade Pod
- Demolition of 2nd Floor Cafeteria Ceilings
- Overhead MEP Rough-In in 2nd Floor Cafeteria
- Demolition of 2nd Floor Kitchen Ceilings
- Installation of 2nd Floor Kitchen Acoustical Ceiling Tile
- Painting of 2nd Floor Kitchen
- Demolition of 3rd Floor Classroom Ceilings
- Painting of 3rd Floor Classrooms
- Interior Courtyard Curtainwall Painting on the 1st Floor
- Water Source Heat Pump Power Distribution for Phase 1A
- Hanging and Finishing Drywall in 5th Grade Pod
- Installation of 3rd Floor Classroom Acoustical Ceiling Tile
- Furring out of 3rd Floor Corridor Walls
- Demolition of 3rd Floor Classroom Flooring
- Interior Courtyard Curtainwall Painting on 3rd Floor
- Sawcut Slab for Curtain Wall Shear Walls on 2nd Floor
- Installation of Light Fixtures in 2nd Floor Cafeteria and East Corridor

HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 07/14/18

CURRENT ACTIVITIES:


- Painting of 3rd Floor Corridors
- Low Voltage Rough-In for Phase 1A
- Installing Flooring in 3rd Grade Classrooms
- Painting 5th Grade Walls
- Frame 5th Grade Ceilings
- Install 5th Grade Ceiling Tile
- Installing Cameras and speakers
- Demolition of 5th Grade Flooring
- Installing 5th Grade Flooring
- Framing 2nd floor Cafeteria and East Corridor Ceilings
- Installing 2nd Floor Cafeteria and East Corridor Ceiling Tile
- Demolition of Cafeteria flooring
- Installing 3rd Floor Corridor Ceiling Tile
- Installation of 3rd Floor Corridor Flooring
- Installing 3rd Floor Classroom Flooring
- Installing Rebar in the Shear Wall Foundation
- Final Cleaning in the Kitchen

HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 07/14/18

PROGRESS PHOTOS:



HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 07/14/18

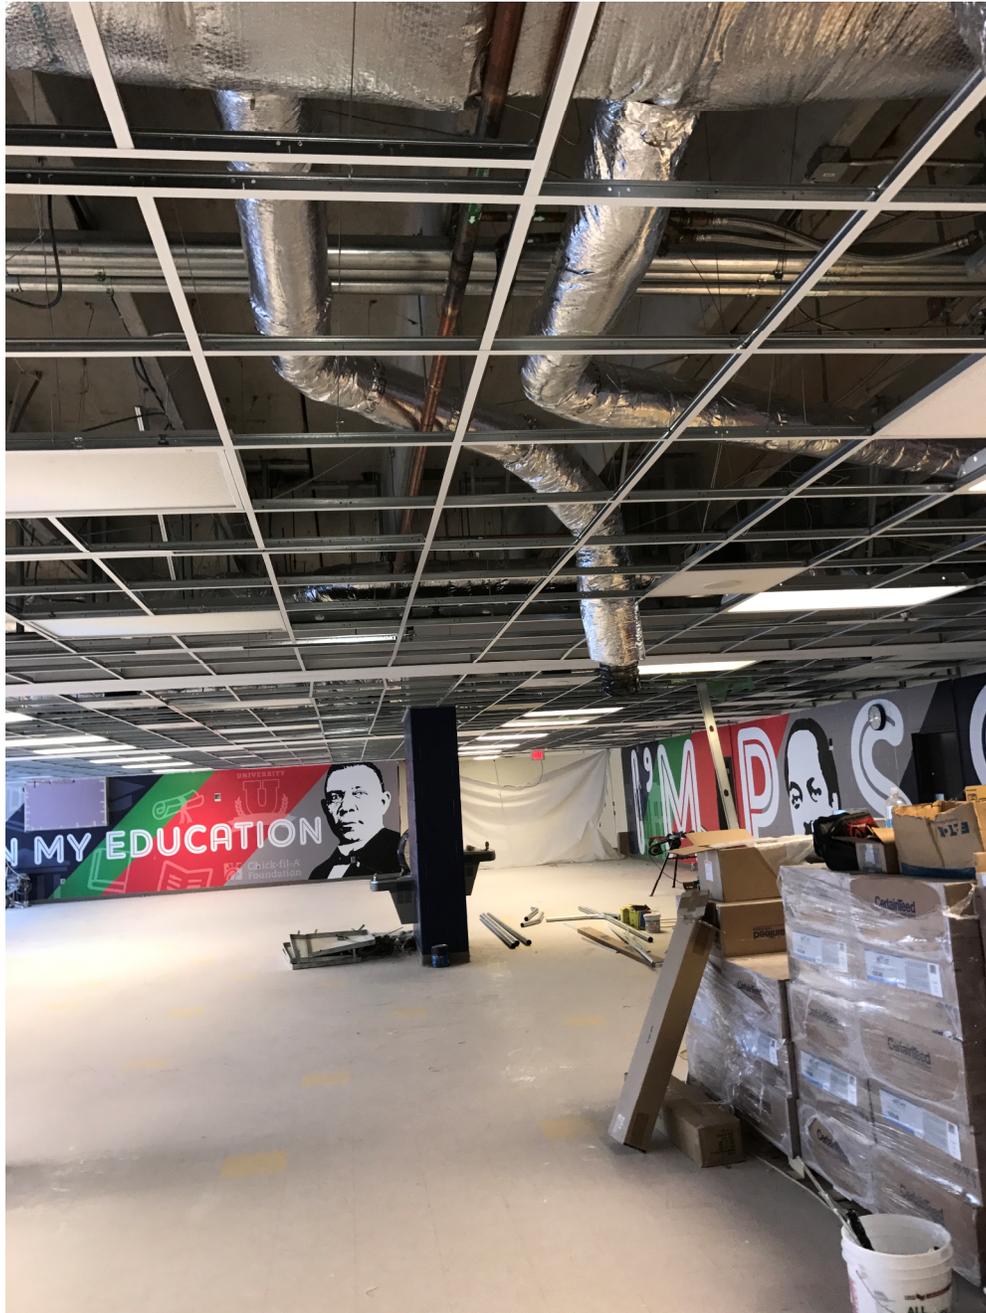

HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 07/14/18



HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 07/14/18





HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 07/14/18

SCHEDULE:

- Substantial Completion Date: July 31, 2019
- Schedule Status: On Schedule

BUDGET:

- Construction Budget: \$8,400,000
