

HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 3/15/19

This Week's Activities:

- 2nd Grade Pod:
 - Install Ceiling Grid in Commons Area
 - Install Lights and Devices
 - Overhead Inspection
- Media Center:
 - Paint Ceiling
 - Install Lights and Devices in the Breakout Rooms
- 3rd Grade Pod:
 - Install Ceiling Grid in Commons Area
- 3rd Floor Corridors:
 - Install Ceiling Grid
- 7th Grade Pod:
 - Hang and Finish Drywall
 - Install Storefronts
- Art/Coding/Tech:
 - Install Steel Posts for Storefronts
 - Electrical Wall Rough In
 - Insulate Duct and Piping
 - In Wall Inspection
 - Hang and Finish Drywall
- 6th Grade Pod:
 - Insulate Duct and Piping
 - Hang and Finish Drywall
 - Install Storefronts
- West Curtainwalls
 - Frame and Pour Shear Walls
 - Install Steel Channels
 - Demo Openings
 - Metal Stud Framing and Sheathing

HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 3/15/19

Next Week's Activities:

- 2nd Grade Pod:
 - Install Ceiling Tile
 - Paint Walls
- Media Center:
 - Paint Walls
- 3rd Grade Pod:
 - Install Lights and Devices
 - Overhead Inspection
- 3rd Floor Corridors:
 - Install Lights and Devices
 - Overhead Inspection
- 7th Grade Pod:
 - Install Ceiling Grid
 - Install Lights and Devices
- Art/Coding/Tech:
 - Hang and Finish Drywall
- 6th Grade Pod:
 - Install Ceiling Grid in Commons Area
 - Install Lights and Devices
- 2nd Floor Corridors
 - Install Ceiling Grid
- West Curtainwalls:
 - Demo Openings
 - Metal Stud Framing and Sheathing
 - Install Waterproofing


HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE

Week Ending 3/15/19

PROGRESS PHOTOS:



HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 3/15/19

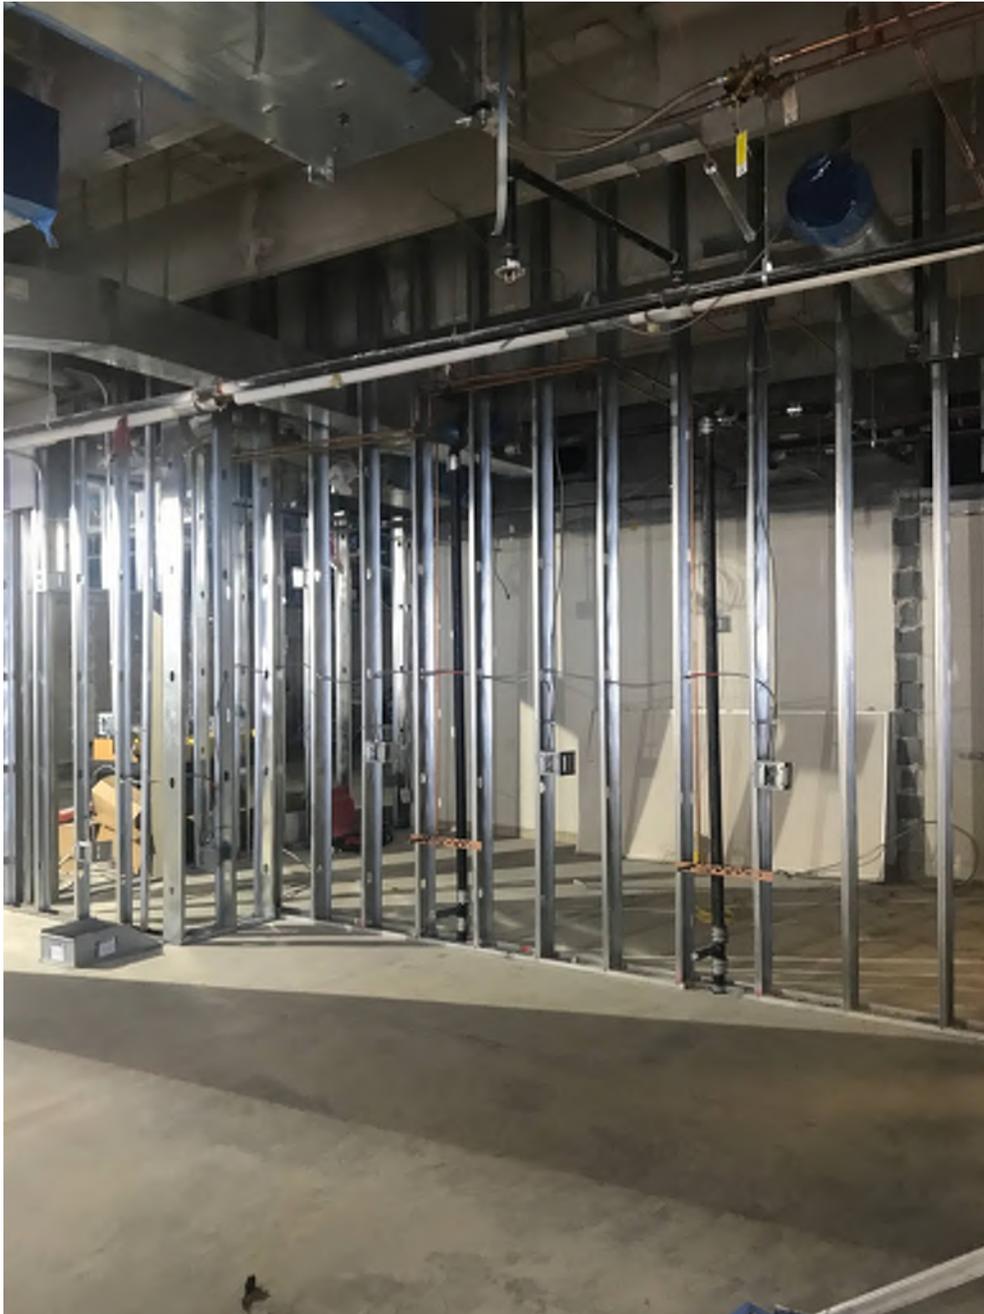

HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 3/15/19



HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 3/15/19



HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 3/15/19





HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 3/15/19

SCHEDULE:

- Substantial Completion Date: June 30, 2019
- Schedule Status: On Schedule

BUDGET:

- Construction Budget: \$8,400,000
- Billed to Date: \$5,568,098.95 (Through 2/28/2019)
