

HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 5/11/19

This Week's Activities:

- 2nd Grade Pod:
 - Final Cleaning

- Media Center:
 - Architectural Tie Ins to the Curtainwalls
 - Ceiling Baffle Mockup

- 3rd Grade Pod:
 - Architectural Tie Ins to the Curtainwalls
 - Final Cleaning

- Art/Coding/Tech:
 - Architectural Tie ins to the Curtainwalls
 - Paint Walls
 - Paint Open Ceiling

- 6th Grade Pod:
 - Architectural Tie ins to the Curtainwalls

- Stairwell #2:
 - Install Lights
 - Demo Railing
 - Install Railing

- Curtainwalls:
 - Install Metal Wall Panels

- Miscellaneous Activities:
 - Complete Pre-Punch Items
 - Correct Items on the QAQC Log

HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 5/11/19

Next Week's Activities:

- Media Center:
 - Install Baffles

- 3rd Grade Pod:
 - Finish Architectural Tie Ins to the Curtainwalls

- 7th Grade Pod:
 - Overhead Inspection
 - Install Ceiling Tile

- Art/Coding/Tech:
 - Overhead Inspection
 - Install Ceiling Tile

- 6th Grade Pod:
 - Finish Architectural Tie Ins to the Curtainwalls
 - Overhead Inspection
 - Install Ceiling Tile

- 2nd Floor Corridors:
 - Overhead Inspection
 - Install Ceiling Tile

- Stairwell #2:
 - Paint Walls

- Curtainwalls:
 - Field Measure for Blinds
 - Field Measure for Coping Caps

- Miscellaneous Areas:
 - Architect to Punch 3rd Floor


**HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE**

Week Ending 5/11/19

PROGRESS PHOTOS:



HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 5/11/19

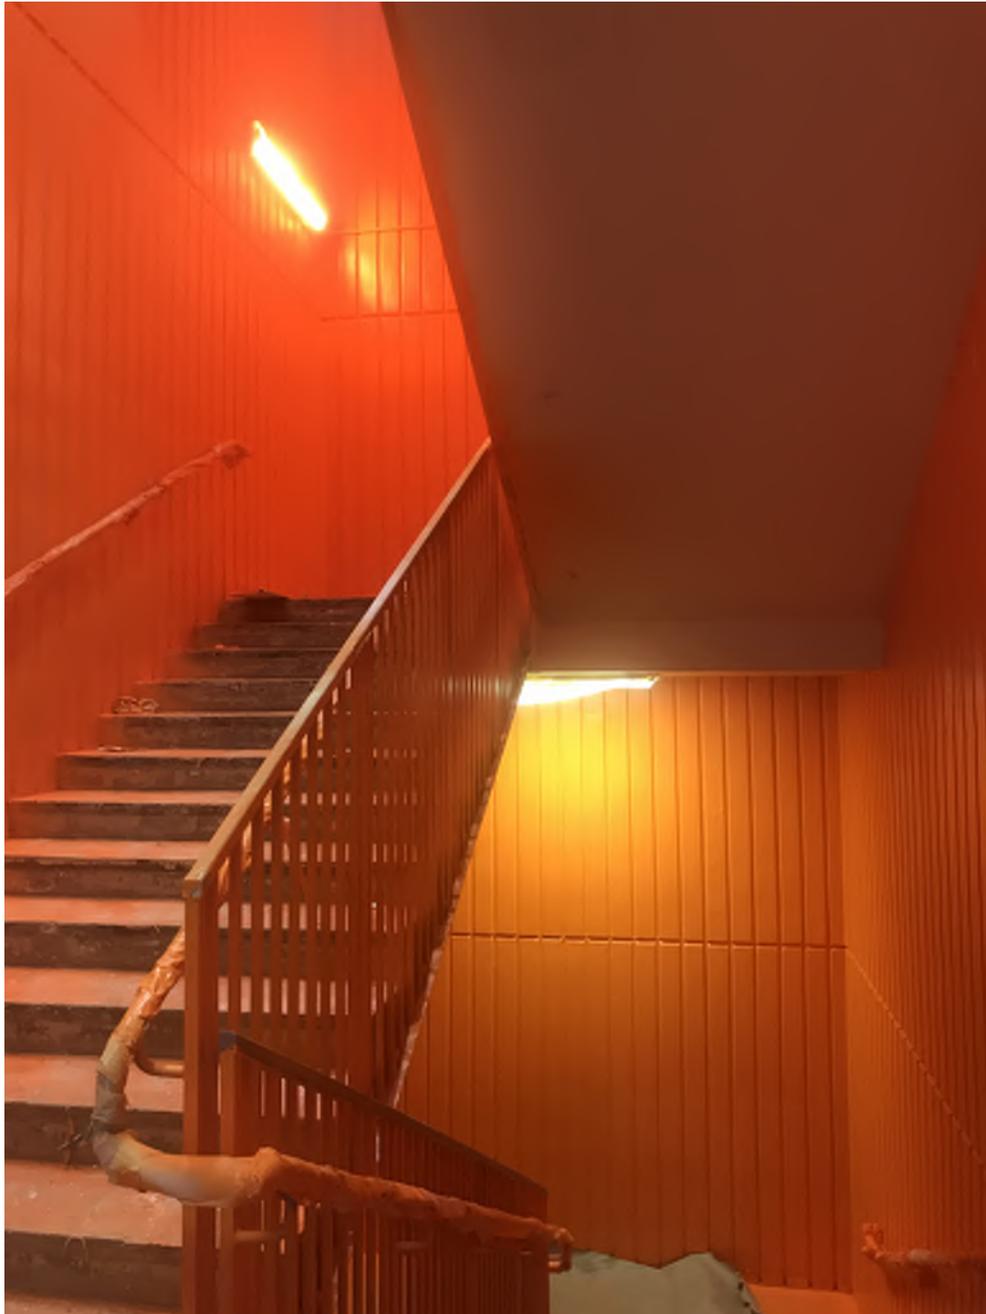

HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 5/11/19



HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 5/11/19





HOLLIS INNOVATION ACADEMY: RENOVATIONS AND MODIFICATIONS
WEEKLY PROGRESS UPDATE
Week Ending 5/11/19

SCHEDULE:

- Substantial Completion Date: June 30, 2019
- Schedule Status: On Schedule

BUDGET:

- Construction Budget: \$8,400,000
- Billed to Date: \$6,975,145.26 (Through 4/30/2019)
