

JACKSON

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 09/04/2023-09/08/2023



Balfour Beatty

Current Activities 09/04/2023-09/08/2023

- Complete
 -
- Started/Ongoing
 - BBC Door Protection
 - Abatement ongoing at the main office
 - BBC need finalized LV Drawings
 - BBC working through Revision 5 Drawings for clarity on scope and discrepancies in demo notes



**Abatement at Main Office
Door Protection Spread**


Upcoming Activities 9/11/23-9/15/23

- Demolition
- Electrical safe-off



Balfour Beatty

Progress Photos

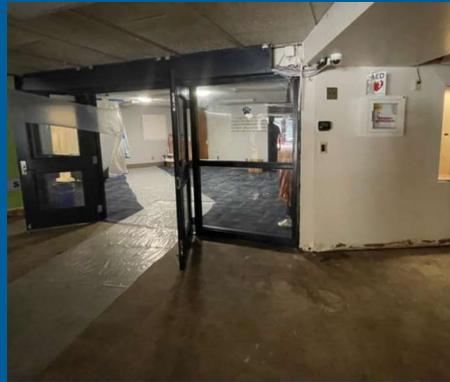

Balfour Beatty

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$12,330,741.00
- Progress Billed to Date: \$562,455.18
- Budget Status: Within GMP



Balfour Beatty
