

# JACKSON ELEMENTARY SCHOOL

*Weekly Construction Progress Report  
Week 6/3/2024-6/7/2024*



**Balfour Beatty**

## Current Activities 6/3/2024-6/7/2024

- **Complete**
  - TPO and Shingle Roof Punch List
  - VCT Complete 2010 Classrooms
  - LVT Complete 2010 Office Spaces
  - Classroom 2010 Waxing VCT
  - Backfill of UG Plumbing at Kitchen
- **Started/Ongoing**
  - APS Move in Furniture in 2010
  - APS Move out of 2020
  - Demo of Ceilings in 2020
  - Site Work for New Grease Traps at Kitchen
  - Demo of Gym Ceilings
  - Corridor Final Paint in 2010
  - Punch List Items in 2010
  - Masonry Blocking and Patch work 2011
  - Toilet Fixture Install 2010/2011
  - Framing and Soffit Install 2011
  - Framing of Grid Ceilings 2011

## Upcoming Activities 6/10/2024-6/14/2024

- Electrical and Mechanical Hard Ceiling Inspection
- Slab on Grade Prep Kitchen
- Slab on Grade Concrete Pour Kitchen
- HVAC Pre – Start Up for Equipment




Backfill Kitchen Area



Grease Trap Install

**Balfour Beatty**

## Progress Photos

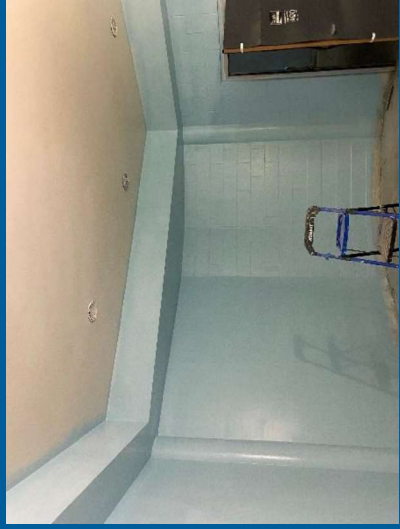



## Project Schedule

- Schedule Status: On Schedule

## Project Financials

- Construction GMP: \$14,833,447.63
- Progress Billed to Date: \$9,945,163.04
- Budget Status: Within GMP



**Balfour Beatty**
