

JACKSON ELEMENTARY SCHOOL

*Weekly Construction Progress Report
Week 6/17/2024-6/21/2024*



Balfour Beatty

Current Activities 6/17/2024-6/21/2024


- **Complete**
 - TPO and Shingle Roof Punch List
 - VCT Complete 2010 Classrooms
 - LVT Complete 2010 Office Spaces
 - Classroom 2010 Waxing VCT
 - Backfill of UG Plumbing at Kitchen
 - Kitchen Concrete Slab
 - Demo of Ceilings in 2020
- **Started/Ongoing**
 - HVAC Pre – Start Up for Equipment
 - Overhead MEP Insulation Kitchen
 - Site Work for New Grease Traps at Kitchen
 - MEP Cover up Lower 2011
 - Waxing Corridor Floors 2010
 - VCT Install 2011 Classrooms
 - Masonry Blocking and Patch Work 2011/Kitchen
 - Toilet Fixture Install 2010/2011
 - Framing and Soffit Install 2011
 - Framing of Grid Ceilings 2011

Upcoming Activities 6/24/2024-6/28/2024

- Ceiling Tile Install 2011 Lower
- Dry-fall Paint Install in Cafeteria and Gym
- Structural Steel Starts in 2020
- Electrical and Mechanical Rough-In




Kitchen Concrete Slab

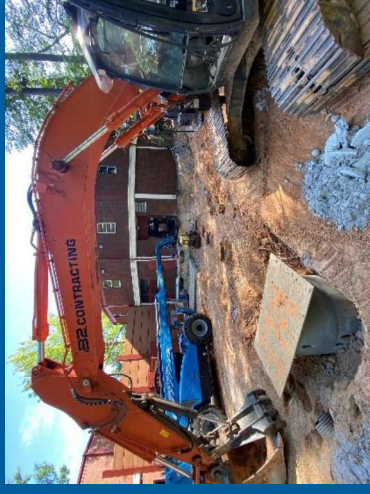

Grease Trap Install

Balfour Beatty

Progress Photos

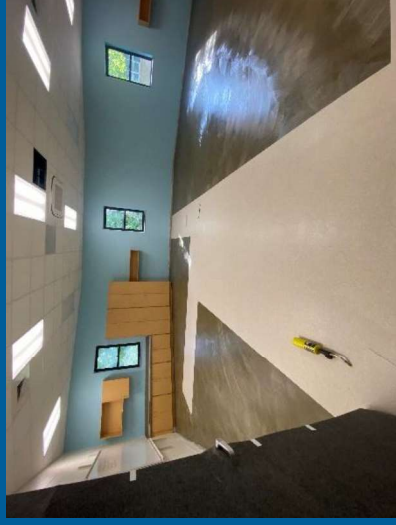



Project Schedule

- Schedule Status: On Schedule

Project Financials

- Construction GMP: \$14,833,447.63
- Progress Billed to Date: \$9,945,163.04
- Budget Status: Within GMP



Balfour Beatty
