

# JACKSON ELEMENTARY SCHOOL

*Weekly Construction Progress Report  
Week 3/4/2024-3/8/2024*



**Balfour Beatty**

## Current Activities 3/4/2024-3/8/2024

- **Complete**
  - Drywall patching around HVAC openings building 2010
  - Roof Drains set
- **Started/Ongoing**
  - Drywall patch building 2010
  - Block point up building 2010
  - Caulking and Primer painting at building 2010
  - Electrical hanging finish lights building 2010
  - Insulation at HVAC piping Building 2010
  - Grilles set at Building 2010
  - Ductwork ongoing at Pods Building 2010
  - HVAC Piping Lower Level at Cafeteria
  - Shingle roofing
  - Demo at kitchen ongoing

## Upcoming Activities 3/11/2024-3/15/2024

- All low voltage wire pulling and rough in devices
- Build new block walls
- MEP rough in kitchen





HVAC Units Set  
Drywall Patching



**Balfour Beatty**

## Progress Photos

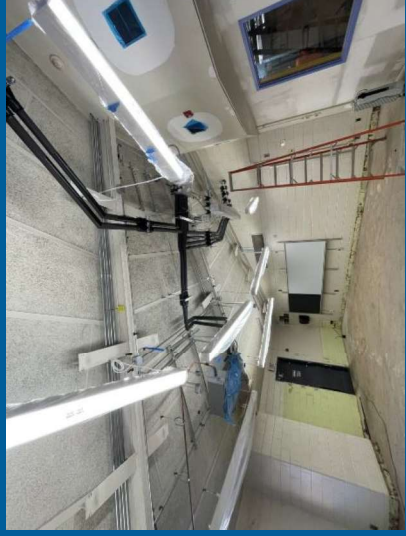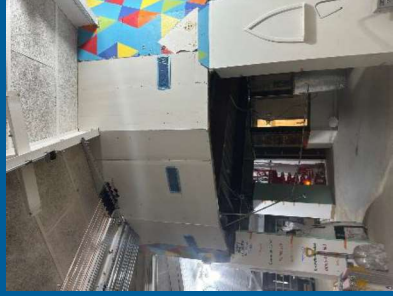

**Balfour Beatty**



## Project Schedule

- Schedule Status: On Schedule

## Project Financials

- Construction GMP: \$12,615,400.40
- Progress Billed to Date: \$4,779,753.12
- Budget Status: Within GMP



**Balfour Beatty**
