

JACKSON ELEMENTARY SCHOOL

*Weekly Construction Progress Report
Week 3/25/2024-3/29/2024*



Balfour Beatty

Current Activities 3/25/2024-3/29/2024

- **Complete**
 - 2011 and 2010 Equipment pads and units set
 - Drywall patch building 2010
 - Block Point up Building 2010
 - Finish Lights hung in classrooms building 2010
 - Demo at Kitchen (with the exception of slab)
- **Started/Ongoing**
 - Electrical Panel install
 - Exterior Paint building 2011
 - Hard ceiling framing Building 2010
 - New block walls at building 2010
 - New door Frames set at building 2010
 - Caulking and Primer painting at building 2010
 - Insulation at HVAC ductwork building 2010
 - Shingle roofing
 - Ductwork and Hood at Kitchen
 - OH MEP Rough at Kitchen

Upcoming Activities 4/1/2024-4/5/2024

- Swap existing Low voltage panels with new panels
- Hang Gypsum Ceilings






New Electrical Panel Install
Hard Ceiling Framing



Balfour Beatty

Progress Photos

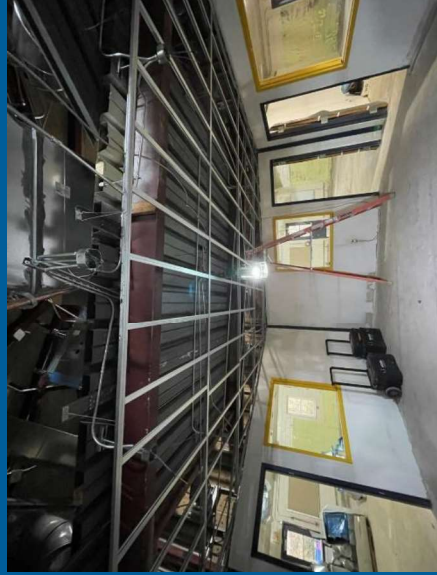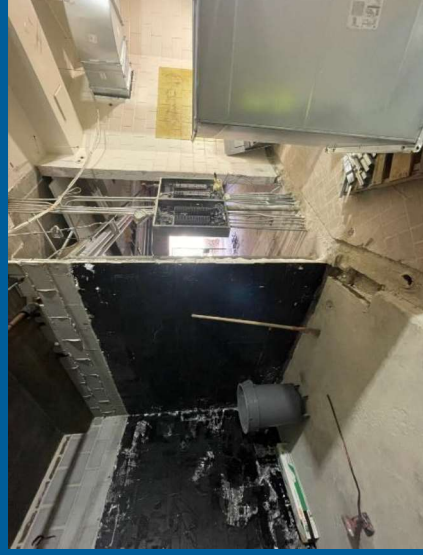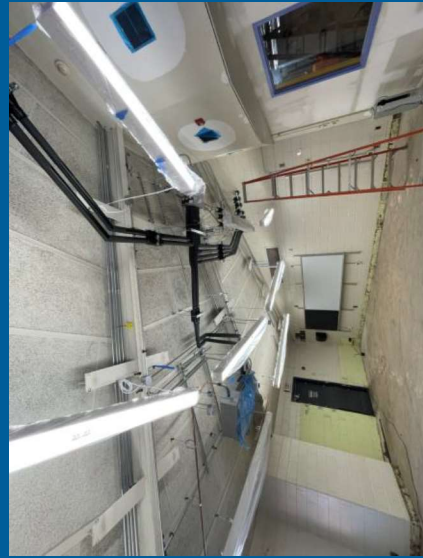



Project Schedule

- Schedule Status: On Schedule

Project Financials

- Construction GMP: \$12,615,400.40
- Progress Billed to Date: \$6,155,098.54
- Budget Status: Within GMP



Balfour Beatty
