

# JACKSON

## ELEMENTARY SCHOOL

*Weekly Construction Progress Report*  
*Week 08/21/2023-08/25/2023*



**Balfour Beatty**

## Current Activities 08/21/2023-08/25/2023

- Complete
  - APS Abatement. All containment has been removed.
- Started/Ongoing
  -



**Abatement Completed**





## Upcoming Activities 8/28/23-9/1/23

- Demolition
- Electrical safe-off



**Balfour Beatty**

Progress Photos

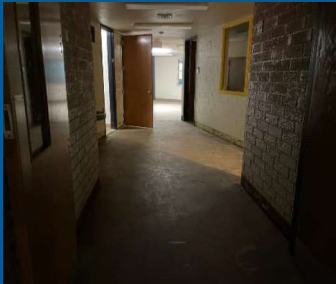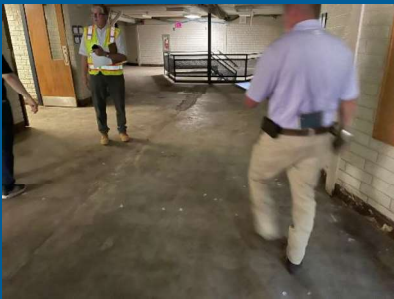

Balfour Beatty

## Project Schedule

- Schedule Status: On Schedule



## Project Financials

- Construction GMP: \$12,330,741.00
- Progress Billed to Date: \$562,455.18
- Budget Status: Within GMP



**Balfour Beatty**
