

JACKSON

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 09/25/2023-09/29/2023



Balfour Beatty

Current Activities 09/25/2023-09/29/2023


- Complete
 - Demo of VCT and Ceiling Tiles upper level
- Started/Ongoing
 - Demo of wall(s) upper level
 - Electrical safe-off
 - Temp. Lighting
 - BBC pending LV Drawings
 - BBC pending Revision 7 Drawings



Demolition ongoing
Door Protection In Place

Upcoming Activities 10/02/23-10/06/23

- Demolition Lower Level
- Electrical safe-off

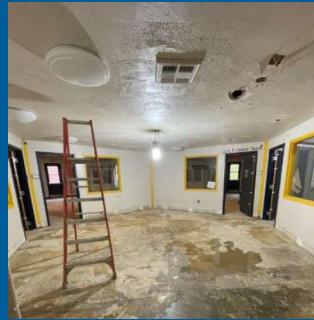

Balfour Beatty

Progress Photos



Balfour Beatty

Project Schedule

- Schedule Status: On Schedule



Project Financials

- Construction GMP: \$12,330,741.00
- Progress Billed to Date: \$644,593.51
- Budget Status: Within GMP



Balfour Beatty
