

JACKSON

ELEMENTARY SCHOOL

Weekly Construction Progress Report
Week 10/16/2023-10/20/2023



Balfour Beatty

Current Activities 10/16/2023-10/20/2023

- Complete
 - HVAC demo partial at 2010 building upper level
 - Temp. Lighting
- Started/Ongoing
 - Electrical safe-off
 - Abatement ongoing at plumbing lines
 - Demo of HVAC
 - BBC Pricing Revision 7 Drawings

Upcoming Activities 10/23/23-10/27/23

- Demolition of casework
- Demo of HVAC and reloop waterpiping




Demolition ongoing



Balfour Beatty

Progress Photos

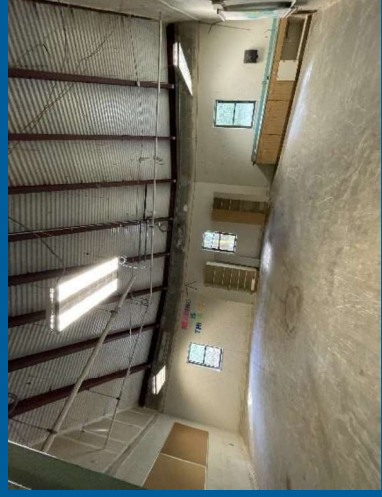



Project Schedule

- Schedule Status: On Schedule

Project Financials

- Construction GMP: \$12,330,741.00
- Progress Billed to Date: \$793,135.38
- Budget Status: Within GMP



Balfour Beatty
