

JACKSON ELEMENTARY SCHOOL

*Weekly Construction Progress Report
Week 10/09/2023-10/13/2023*




Balfour Beatty

Current Activities 10/09/2023-10/13/2023

- Complete
 - Demo ceiling tiles lower level
 - Abatement complete at carpeted rooms
 - Plumbing disconnected
- Started/Ongoing
 - Electrical safe-off
 - Temp. Lighting
 - HVAC demo upper level
 - Demo of hard ceilings upper level
 - Abatement ongoing at plumbing lines
 - BBC Pricing Revision 7 Drawings

Upcoming Activities 10/16/23-10/20/23

- Demolition of casework
- Demo of HVAC and reloop waterpiping


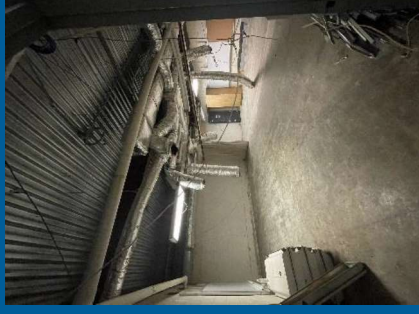


Demolition ongoing
HVAC Demo ongoing



Balfour Beatty

Progress Photos

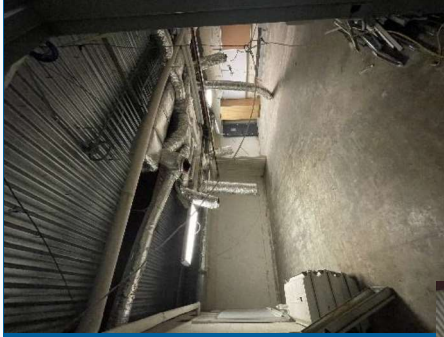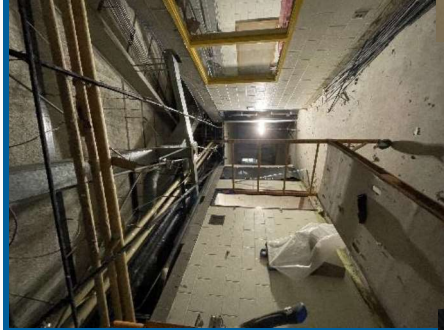



Project Schedule

- Schedule Status: On Schedule

Project Financials

- Construction GMP: \$12,330,741.00
- Progress Billed to Date: \$793,135.38
- Budget Status: Within GMP



Balfour Beatty
