

JACKSON ELEMENTARY SCHOOL

*Weekly Construction Progress Report
Week 12/11/2023-12/15/2023*



Balfour Beatty

Current Activities 12/11/2023-12/15/2023

- **Complete**
 - Hanging of Branch Selector at Upper Level building 2011
 - Ductwork Upper Level building 2011
 - HVAC piping at Upper Level building 2011
 - Received delivery of DOAS units
- **Started/Ongoing**
 - Electrical tie-in ongoing for mechanical units
 - Hanging FCU Upper Level Building 2010
 - Demo of Artroom (Balfour Beatty has moved out completely)

Upcoming Activities 12/18/2023-12/22/2023

- HVAC piping at Upper Level building 2010
- Ductwork Upper Level building 2010
- Demo of Roofing and begin Reroof
- Pour Equipment Pads
- Install temporary partition at Kitchen/Cafeteria




HVAC Rough-in Ongoing
Demo Complete



Balfour Beatty

Progress Photos

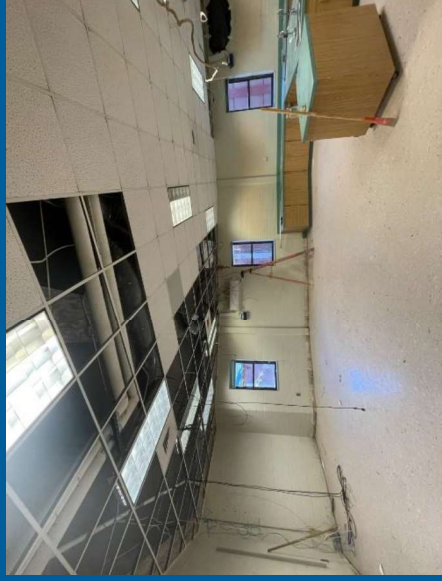



Project Schedule

- Schedule Status: On Schedule

Project Financials

- Construction GMP: \$12,330,741.00 (pending GMP #3 amendment execution)
- Progress Billed to Date: \$2,033,580.27
- Budget Status: Within GMP



Balfour Beatty
