

JACKSON ELEMENTARY SCHOOL

*Weekly Construction Progress Report
Week 1/15/2024-1/19/2024*



Balfour Beatty

Current Activities 1/15/2024-1/19/2024

- **Complete**
 - Hanging FCU Lower Level Building 2011
- **Started/Ongoing**
 - Electrical tie-in ongoing for mechanical units
 - Electrical rough-in for low voltage
 - Demo of Roofing and begin Reroof
 - HVAC Piping at Principal office
 - HVAC Piping Lower Level Building 2011
 - Insulation at HVAC piping upper level Building 2011
 - Demo of restroom ceilings at kitchen (in contract scope)

Upcoming Activities 1/22/2024-1/26/2024

- VRV unit connection and ductwork Building 2010
- Low voltage to begin pulling new wire
- Pour Equipment Pads





Electrical Rough-in Ongoing
Demo at Kitchen



Balfour Beatty

Progress Photos

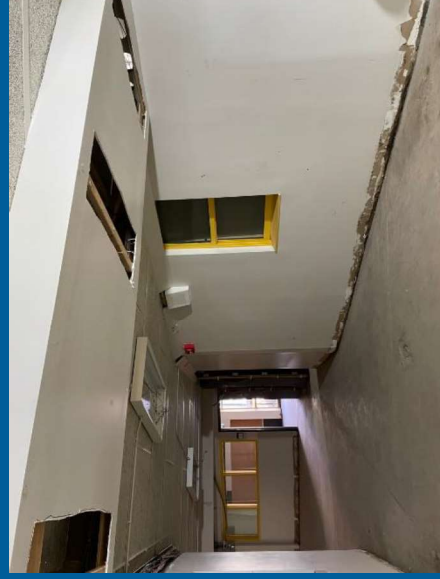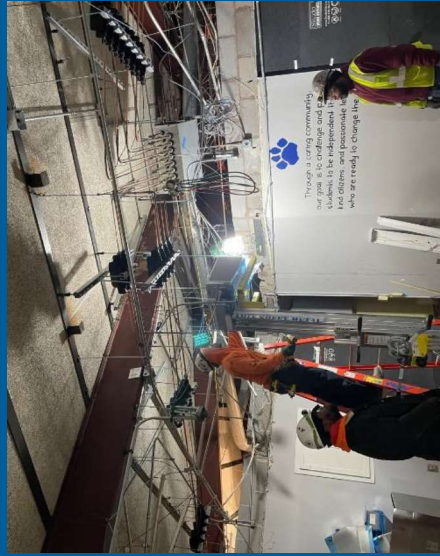



Project Schedule

- Schedule Status: On Schedule

Project Financials

- Construction GMP: \$12,330,741.00 (pending GMP #3 amendment execution)
- Progress Billed to Date: \$2,835,983.77
- Budget Status: Within GMP



Balfour Beatty
