

# JACKSON ELEMENTARY SCHOOL

*Weekly Construction Progress Report  
Week 11/06/2023-11/10/2023*




**Balfour Beatty**

## Current Activities 11/06/2023-11/10/2023

- Complete
- Started/Ongoing
  - Demo of casework and shelving
  - Demo of hard ceilings at restrooms
  - Electrical rough-in upper level building 2010
  - Electrical rough-in in Mech. Room
  - HVAC rough-in
  - Abatement and containment for plumbing lines
  - BBC Pricing Revision 7 Drawings
  - BBC Pricing Revision 8 Drawings

## Upcoming Activities 11/13/2023-11/17/2023

- Demo of HVAC in media center and reloop waterpiping
- HVAC rough-in
- Demo of remaining carpet
- Once abatement is complete – demo plumbing fixtures

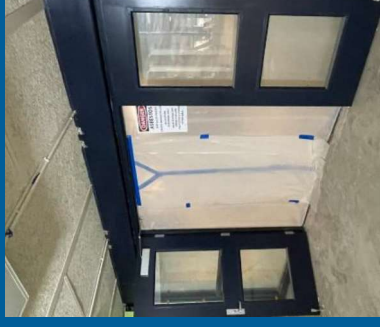


Demolition ongoing  
Rough-in Ongoing



**Balfour Beatty**

# Progress Photos

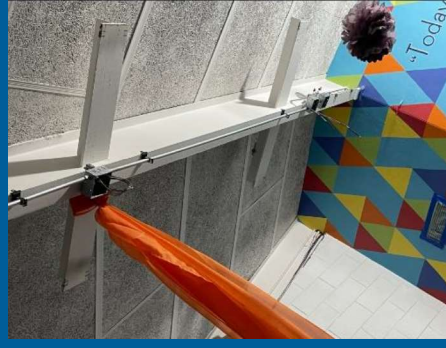



## Project Schedule

- Schedule Status: On Schedule

## Project Financials

- Construction GMP: \$12,330,741.00
- Progress Billed to Date: \$1,526,692.67
- Budget Status: Within GMP



**Balfour Beatty**
