


Project name: EV Charging Station (Metro Bus Facility)

DATE OF THE REPORT 10/13/2023

Initial information	Data
PROJECT BUDGET (GMP)	\$788,000.00 +68,000.00 (POLE WITH CAMERAS- NO NTP/P.O.)
START DATE	06/15/2023
COMPLETION DATE	03/17/2024
NAME OF THE CMAR	BROWN AND ROOT
PROJECT MANAGER FROM CMAR	ANTHONY JORDAN
PROJECT MANAGER FROM APS	ALEX REVIN

1. PROJECT OVERVIEW

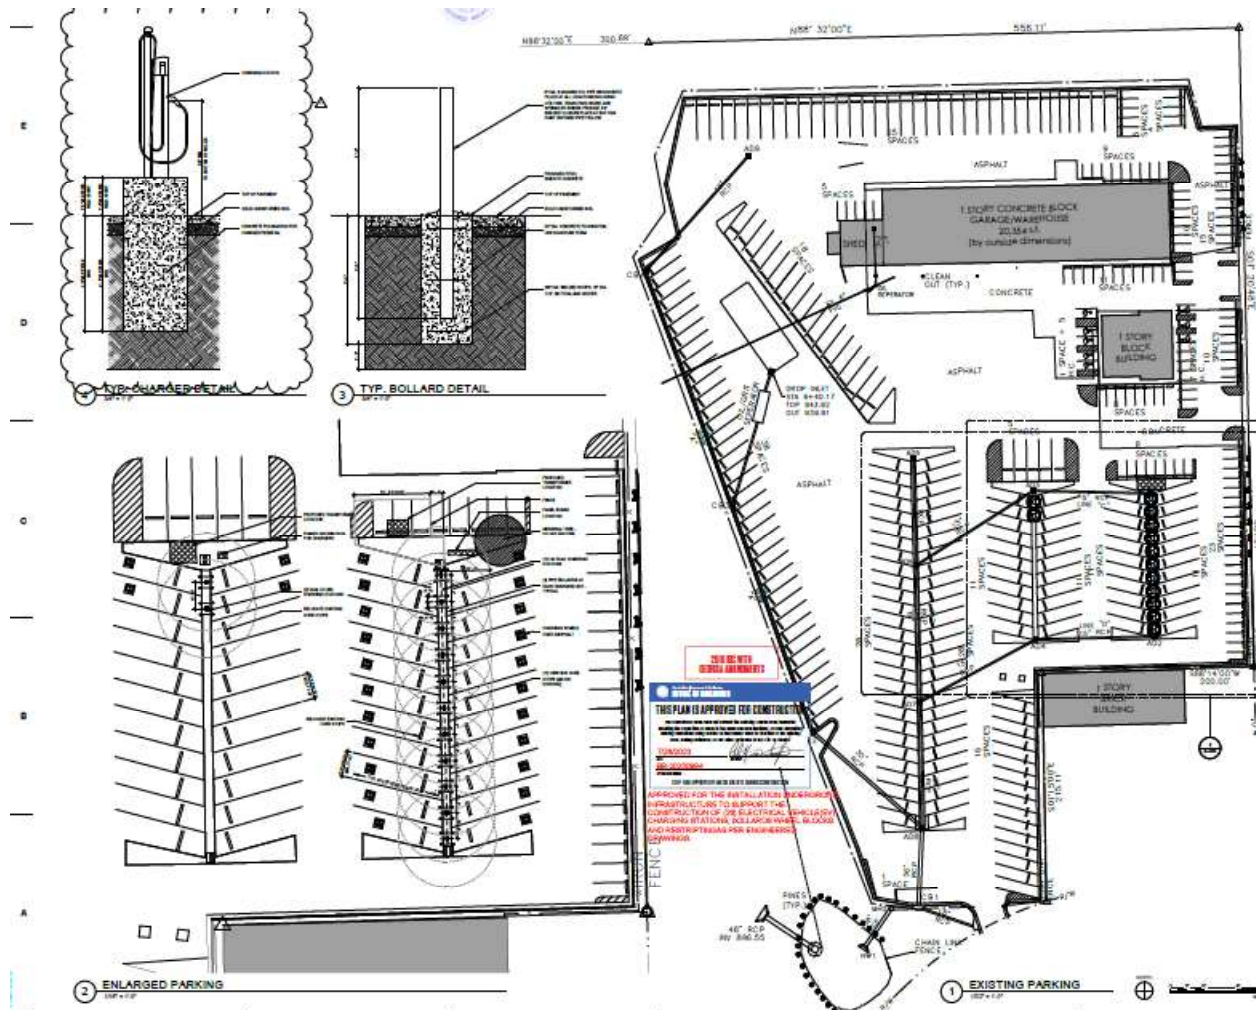

SCOPE OF WORK: CURRENT WEEK

- ERECTING FORMS FOR FOOTERS/PADS
- AWAITING DELIVERY OF ANCHOR BOLT TEMPLATES FOR DC CHARGING STATIONS

SCOPE OF WORK: NEXT WEEK

- CONTINUE ERECTING FORMS, INSTALLING ANCHOR BOLT TEMPLATES & REBAR FOR FOOTERS/PADS FOR CHARGING STATIONS

ISSUES- NEED OFFICIAL NOTICE TO PROCEED FOR THE CAMERA POLES, IN ORDER FOR MATERIALS/EQUIPMENT TO BE ORDERED/PROCURED AND WORK TO BE PERFORMED





