


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit center

WEEK ENDING 12/08/2023

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	07/31/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

PROJECT OVERVIEW

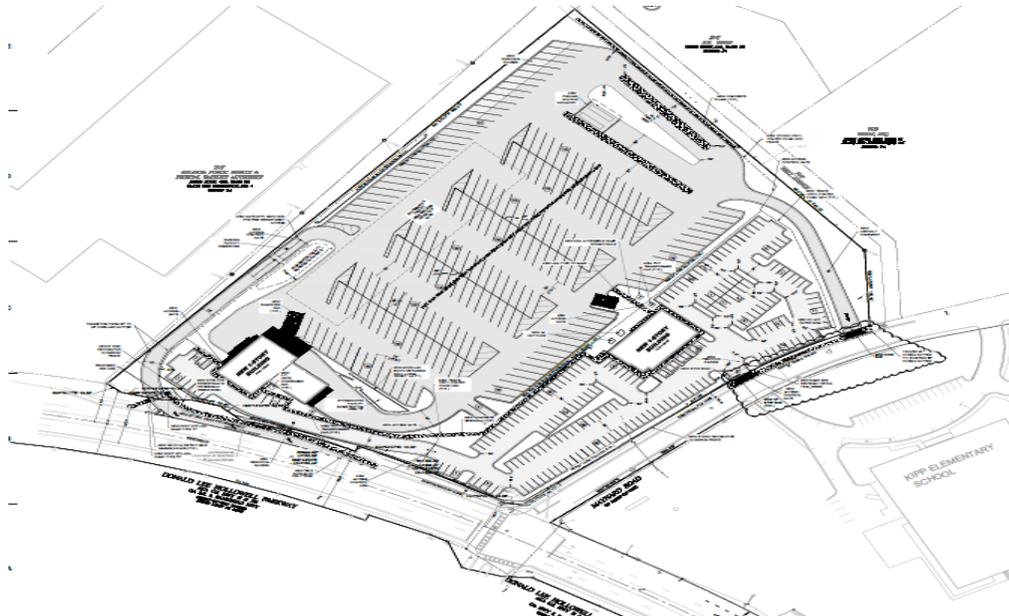

Construction Activities this week

- 50% COMPLETED WITH BIORETENTION
- 50% COMPLETED WITH STORM LINES/STRUCTURES
- BUILDING PAD PREP
- COORDINATING A LOGISTICS PLAN FOR SS BORE ACROSS MAYNARD STREET
- EXCAVATING THE RETENTION BASIN.
- UNDERGROUND RETENTION SITE PREP

CONSTRUCTION ACTIVITIES PLANNED (5 WEEK LOOK AHEAD)

THIS IS DEPENDENT UPON BUILDING PERMIT STATUS AND WEATHER.

- CONCRETE, REBAR, PLUMBING & ELECTRICAL EQUIPMENT DELIVERIES
- STRUCTURAL FOUNDATION LAYOUT
- CONTINUE TO WORK ON BUILDING PADS
- UNDERSLAB PLUMBING INSTALLATION (MEP INSTALLATION)
- CONCRETE WORK/POUR SLABS
- SANITARY & WATER UTILITIES TO BEGIN NEXT WEEK.

MANPOWER LOG (WEEK OF 12/08/23)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	25	24	22	20	15

WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT

