


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit Center

WEEK ENDING 03/15/2024

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	08/09/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

PROJECT OVERVIEW

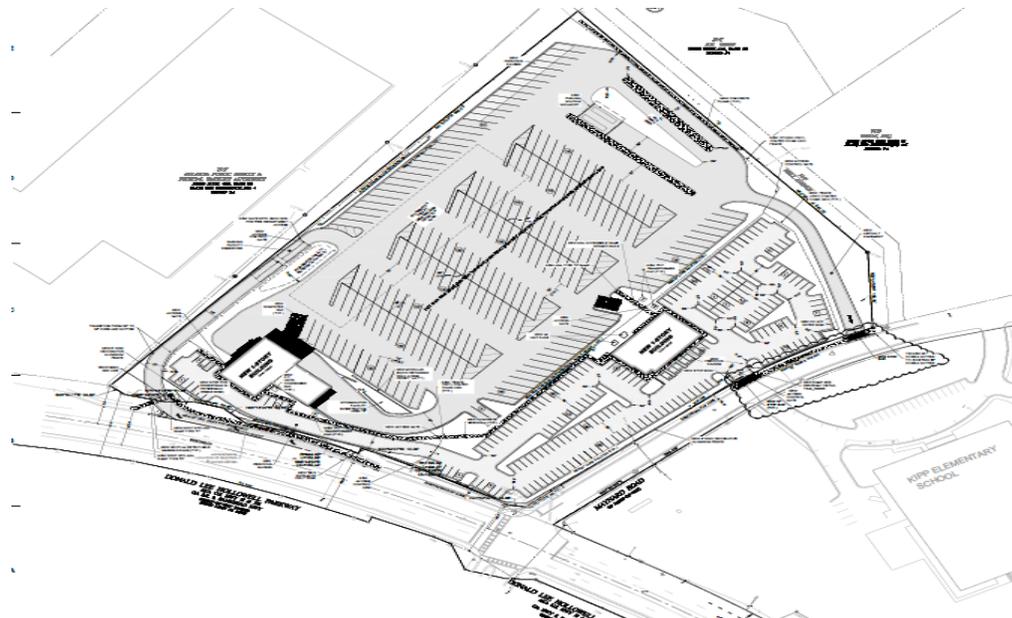

Construction Activities this week

- GDOT PERMIT IS IN FINAL STAGES OF PROCESSING.
- 100% OF MASS GRADING FOR LAYDOWN AREA IS COMPLETE. EQUIPMENT AND CONEX BOXES HAVE ARRIVED ONSITE. GRAVEL HAS BEEN LAID.
- SITE INFRASTRUCTURE CONSTRUCTION IS ROUGHLY 85 % INSTALLED.
- MODULAR BLOCK WALL "C" INSTALLATION IS ONGOING. WALLS "A" & "B" ARE IN PLANNING.
- SUBGRADE EXCAVATION IS ONGOING, NEAR COMPLETION.
- UNDERGROUND ELECTRICAL & IRRIGATION SITEWORK IS ONGOING.
- CURB & GUTTER LAYOUT HAS COMMENCE. CURBS WILL BE FORMED NEXT WEEK.
- OPERATIONS PEMB (PRE-ENGINEERED METAL BUILDING) HAS ARRIVED ONSITE (03/15/24). PLEASE SEE PICTURES BELOW FOR REFERENCE.

CONSTRUCTION ACTIVITIES PLANNED (5 WEEK LOOK AHEAD)

THIS IS DEPENDENT UPON PERMITTING STATUS AND WEATHER.

- MAINTENANCE BUILDING PEMB TRACKING FOR (04-12-24).
- STEEL ERECTION
- START EXTERIOR/INTERIOR CONSTRUCTION OF THE OPERATIONS BUILDING
- CURB & GUTTER INSTALLATION.
- CMU INSTALLATIONS.
- MAINTENANCE BUILDING SLAB POURED.
- SITE CONSTRUCTION (I.E. LIGHT POLES/ CHARGING STATIONS/ IRRIGATION)
- PAVING/PERMEABLE PAVING SUB BASE
- SANITARY & WATER UTILITIES SCOPE OF WORK CONTINUED.

WEEKLY CONSTRUCTION PROGRESS REPORT



MANPOWER LOG (WEEK OF 03/15/24)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	18	18	18	18	2
JAMISON CONSTRUCTION	12	12	12	12	12
PENCO ELECTRICAL	4	4	4	4	4
TEBARCO MECHANICAL	4	4	4	4	2
NOVA ENGINEERING	2	2	2	2	1
THE PAINT DOCTOR	2	2	2	2	2
FOX METAL BUILDING COMPANY	4	4	4	4	4

WEATHER LOG (MONTH OF DECEMBER/JANUARY/FEBRUARY/MARCH)

- UP TO DATE, APS NW TRANSPORTATION CENTER HAS HAD (34) THIRTY-FOUR TRACKED RAIN DAYS IN DECEMBER/JANUARY/FEBRUARY/MARCH.
- DAYS LOGGED: (12-01-23) / (12-02-23) / (12-03-23) / (12-08-23) / (12-09-23) / (12-10-23) / (12-24-23) / (12-25-23) / (12-26-23) / (01/06/24) / (01/08/24) / (01/09/24) / (01/12/24) / (01/16/24) / (01/19/24) / (01/24/24) / (01/25/24) / (01/26/24) / (01/27/24) / (01/28/24) / (01/29/24) / (02/04/24) / (02/10/24) / (02/11/24) / (02/12/24) / (02/22/24) / (02/28/24) / (03/01/24) / (03/04/24) / (03/05/24) / (03/06/24) / (03/08/24) / (03/10/24) / (03/15/24)
- TRACKED INCLEMENT CONDITIONS DAYS: 44 DAYS

WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT

