


# WEEKLY CONSTRUCTION PROGRESS REPORT

## Project name: Northwest Bus Transit Center

WEEK ENDING 04/05/2024

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	08/09/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

### PROJECT OVERVIEW

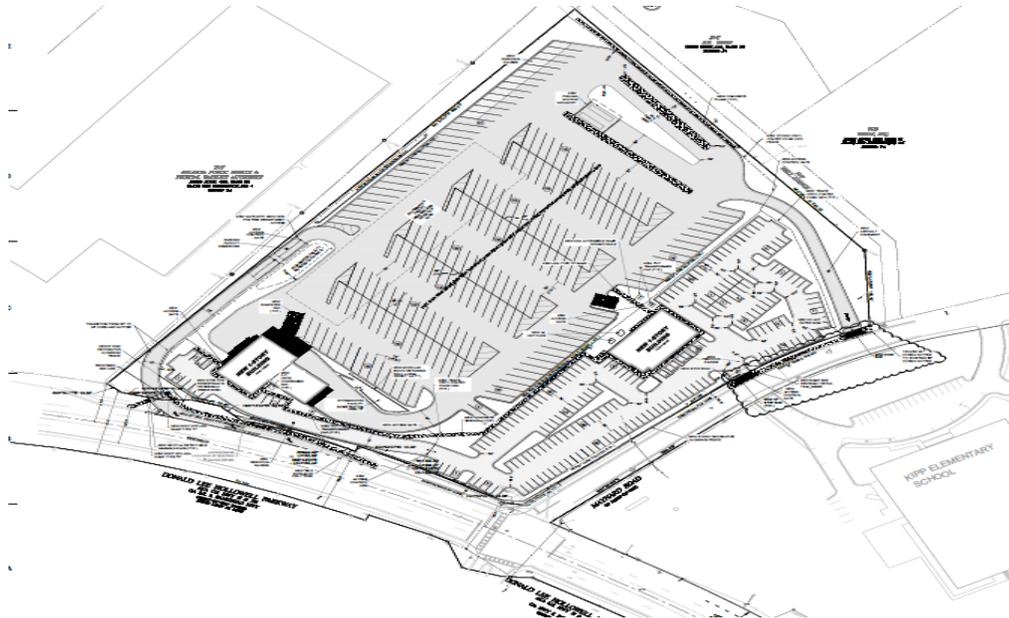

---

### Construction Activities this week

- GDOT PERMIT IS IN FINAL STAGES OF PROCESSING.
- SITE INFRASTRUCTURE CONSTRUCTION IS ROUGHLY 85 % INSTALLED.
- MODULAR BLOCK WALL "C" INSTALLATION HAS BEEN COMPLETED. WALLS "A" HAS ALSO BEEN COMPLETED. WALL "B" IS ONGOING.
- SUBGRADE EXCAVATION IS ONGOING, NEAR COMPLETION.
- UNDERGROUND ELECTRICAL & IRRIGATION SITEWORK IS ONGOING.
- CURB & GUTTER LAYOUT HAS COMMENCE. CURBS & GUTTER INSTALLATION SCHEDULED TO START NEXT WEEK DEPENDING UPON WEATHER.
- MAINTENANCE BUILDING PAD IN PREPARATION FOR STEEL DELIVERY.
- OPERATIONS PEMB ERECTION IS ONGOING.
- OPERATIONS INTERIOR/EXTERIOR WALL FRAMING ONGOING.
- MEP TRADES PLUMBING ROUGH-INS ONGOING

### CONSTRUCTION ACTIVITIES PLANNED (5 WEEK LOOK AHEAD)

**THIS IS DEPENDENT UPON PERMITTING STATUS AND WEATHER.**

- MAINTENANCE BUILDING PEMB TRACKING FOR (04-12-24).
- CURB & GUTTER INSTALLATION.
- SITE CONSTRUCTION (I.E. LIGHT POLES/ CHARGING STATIONS/ IRRIGATION)
- SANITARY & WATER UTILITIES SCOPE OF WORK CONTINUED.
- FENCE INSTALLATION IS IN THE PROCESS OF BEING COORDINATED.
- GA POWER COORDINATION IS ONGOING.
- REMAINING SITE DEMOLITION ONGOING.
- LANDSCAPING AND IRRIGATION SYSTEM COORDINATION IS ONGOING.
- FUELING STATION SCOPE TO BE SCHEDULED. PENDING FINAL DESIGN COORDINATION.
- LIGHTPOLE INSTALLATION SCHEDULED WEEK OF (04/13/24).

## WEEKLY CONSTRUCTION PROGRESS REPORT



### MANPOWER LOG (WEEK OF 04/05/24)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	18	18	18	18	18
PENCO ELECTRICAL	4	4	4	4	4
TEBARCO MECHANICAL	2	2	2	2	2
NOVA ENGINEERING	1	1	1	1	1
VISIONSCAPES	1	1	1	1	1
FOX BUILDING COMPANY	2	2	2	2	2
GEA	2	2	2	2	2

### WEATHER LOG (MONTH OF DECEMBER/JANUARY/FEBRUARY/MARCH)

- UP TO DATE, APS NW TRANSPORTATION CENTER HAS HAD (37) THIRTY-SEVEN TRACKED RAIN DAYS IN DECEMBER/JANUARY/FEBRUARY/MARCH/APRIL.
- DAYS LOGGED: (12-01-23) / (12-02-23) / (12-03-23) / (12-08-23) / (12-09-23) / (12-10-23) / (12-24-23) / (12-25-23) / (12-26-23) / (01/06/24) / (01/08/24) / (01/09/24) / (01/12/24) / (01/16/24) / (01/19/24) / (01/24/24) / (01/25/24) / (01/26/24) / (01/27/24) / (01/28/24) / (01/29/24) / (02/04/24) / (02/10/24) / (02/11/24) / (02/12/24) / (02/22/24) / (02/28/24) / (03/01/24) / (03/04/24) / (03/05/24) / (03/06/24) / (03/08/24) / (03/10/24) / (03/15/24) / (03/22/24) / (03/26/24) / (04/02/24)
- TRACKED INCLEMENT CONDITIONS DAYS: 49 DAYS

WEEKLY CONSTRUCTION PROGRESS REPORT



# WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT

