


# WEEKLY CONSTRUCTION PROGRESS REPORT

## Project name: Northwest Bus Transit Center

WEEK ENDING 04/19/2024

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	08/09/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

### PROJECT OVERVIEW

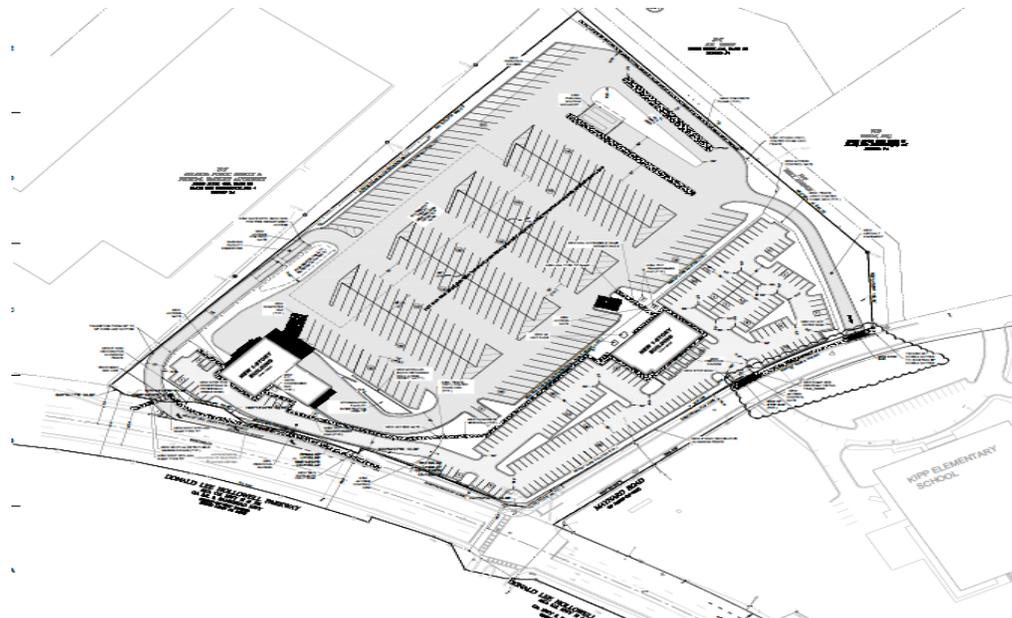

---

### Construction Activities this week

- GDOT PERMIT RECEIVED.
- SITE INFRASTRUCTURE CONSTRUCTION IS ROUGHLY 85 % INSTALLED.
- FINAL GRADING NEAR COMPLETE.
- UNDERGROUND ELECTRICAL & IRRIGATION SITework IS ONGOING.
- CURB & GUTTER SCOPE HAS BEGUN. PLEASE SEE IN PHOTOS BELOW.
- MAINTENANCE BUILDING ERECTION HAS COMMENCE. PLEASE SEE IN PHOTOS BELOW.
- OPERATIONS PEMB ERECTION IS ONGOING.
- OPERATIONS INTERIOR/EXTERIOR WALL FRAMING ONGOING.
- MEP TRADES PLUMBING ROUGH-INS ONGOING
- NEW GA POWER POLES HAVE BEEN PLACED ONSITE

### CONSTRUCTION ACTIVITIES PLANNED (5 WEEK LOOK AHEAD)

**THIS IS DEPENDENT UPON PERMITTING STATUS AND WEATHER.**

- CURB & GUTTER INSTALLATION.
- SITE CONSTRUCTION (I.E. LIGHT POLES/ CHARGING STATIONS/ IRRIGATION)
- SANITARY & WATER UTILITIES SCOPE OF WORK CONTINUED.
- FENCE INSTALLATION IS IN THE PROCESS OF BEING COORDINATED.
- GA POWER COORDINATION IS ONGOING.
- REMAINING SITE DEMOLITION ONGOING.
- LANDSCAPING AND IRRIGATION SYSTEM COORDINATION IS ONGOING.
- FUELING STATION SCOPE TO BE SCHEDULED. PENDING FINAL DESIGN COORDINATION.
- LIGHTPOLE INSTALLATION SCHEDULED WEEK OF (04/26/24).

## WEEKLY CONSTRUCTION PROGRESS REPORT





### MANPOWER LOG (WEEK OF 04/19/24)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	18	8	8	8	18
PENCO ELECTRICAL	4	2	2	2	4
TEBARCO MECHANICAL	2	2	2	2	2
NOVA ENGINEERING	1	1	1	1	1
VISIONSCAPES	1	1	1	1	1
JAMISON CONSTRUCTION	6	6	6	6	6
FOX BUILDING COMPANY	7	7	7	7	7
GEA	6	6	6	6	6

### WEATHER LOG (MONTH OF DECEMBER/JANUARY/FEBRUARY/MARCH/APRIL)

- UP TO DATE, APS NW TRANSPORTATION CENTER HAS HAD (43) FORTY-THREE TRACKED RAIN DAYS IN DECEMBER/JANUARY/FEBRUARY/MARCH/APRIL.
- DAYS LOGGED: (12-01-23) / (12-02-23) / (12-03-23) / (12-08-23) / (12-09-23) / (12-10-23) / (12-24-23) / (12-25-23) / (12-26-23) / (01/06/24) / (01/08/24) / (01/09/24) / (01/12/24) / (01/16/24) / (01/19/24) / (01/24/24) / (01/25/24) / (01/26/24) / (01/27/24) / (01/28/24) / (01/29/24) / (02/04/24) / (02/10/24) / (02/11/24) / (02/12/24) / (02/22/24) / (02/28/24) / (03/01/24) / (03/04/24) / (03/05/24) / (03/06/24) / (03/08/24) / (03/10/24) / (03/15/24) / (03/22/24) / (03/26/24) / (04/02/24) / (04/08/24) / (04/09/24) / (04/10/24) / (04/11/24) / (04/17/24) / (04/19/24)
- TRACKED INCLEMENT CONDITIONS DAYS: 56 DAYS

WEEKLY CONSTRUCTION PROGRESS REPORT


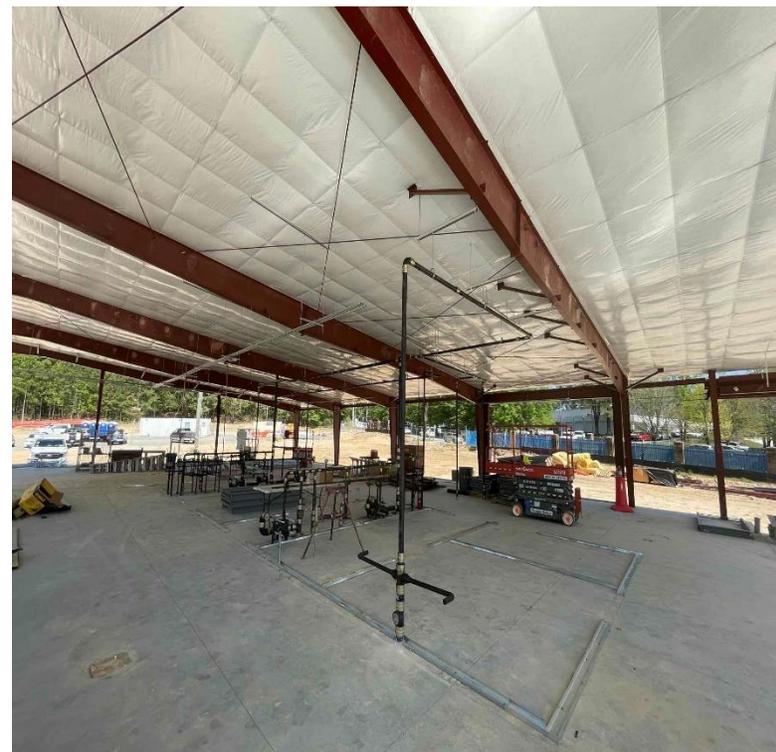
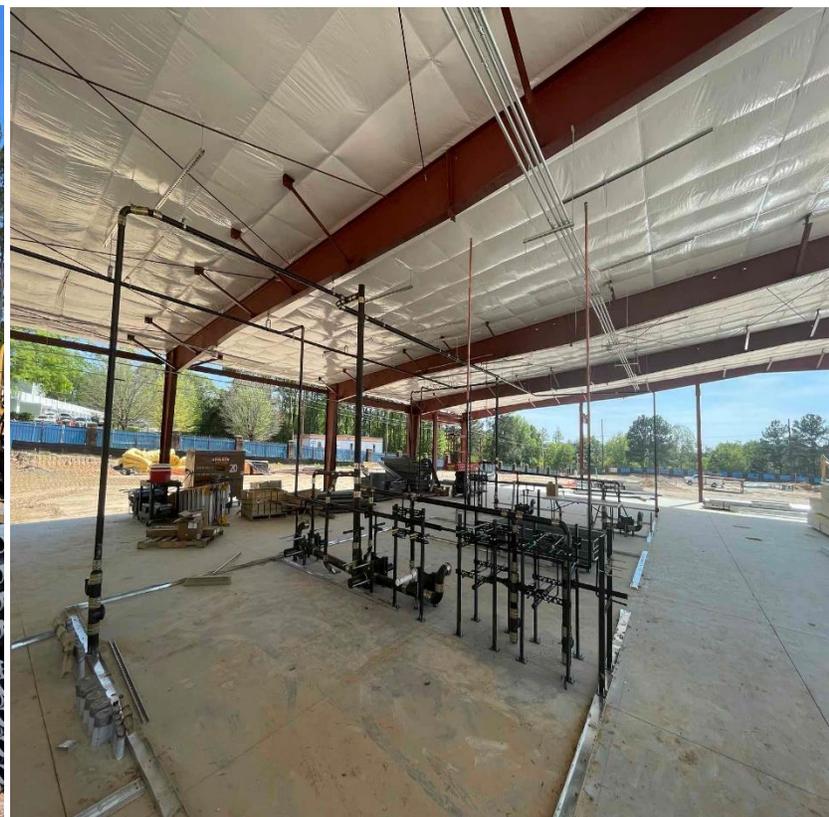


WEEKLY CONSTRUCTION PROGRESS REPORT

Ajax



ATLANTA  
PUBLIC  
SCHOOLS

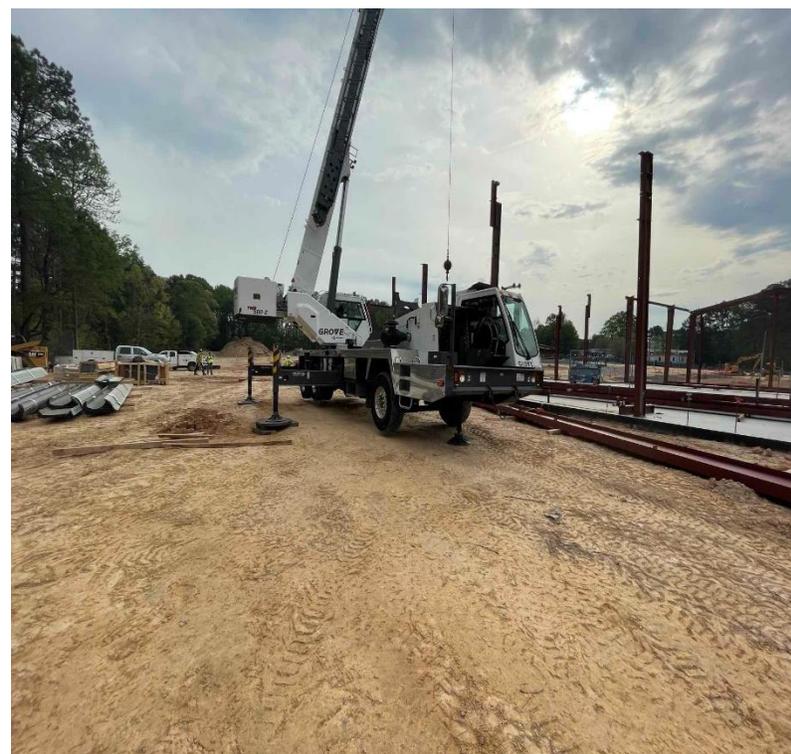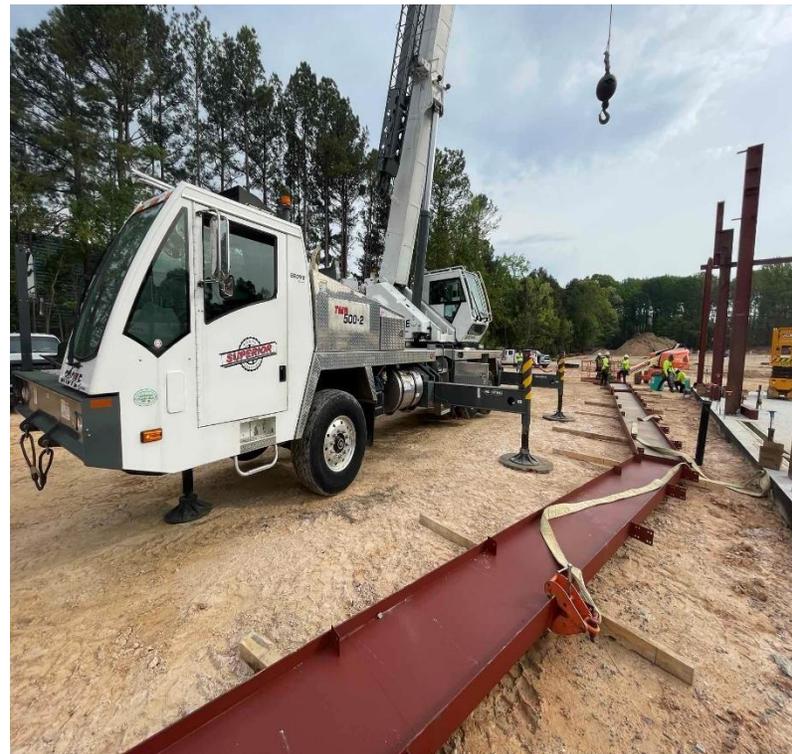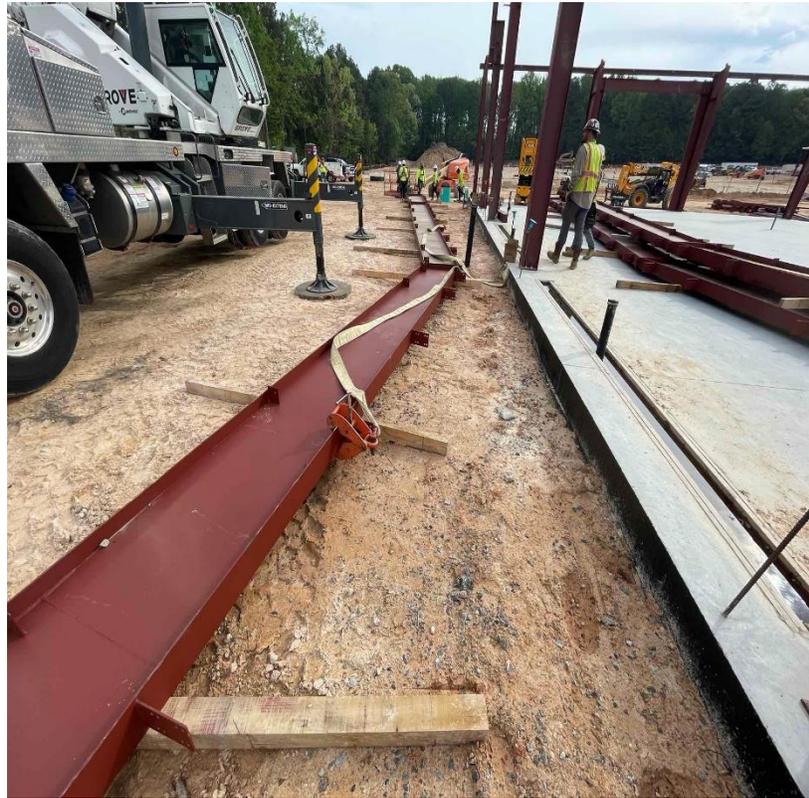

WEEKLY CONSTRUCTION PROGRESS REPORT

