


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit Center

WEEK ENDING 05/10/2024

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	08/09/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

PROJECT OVERVIEW

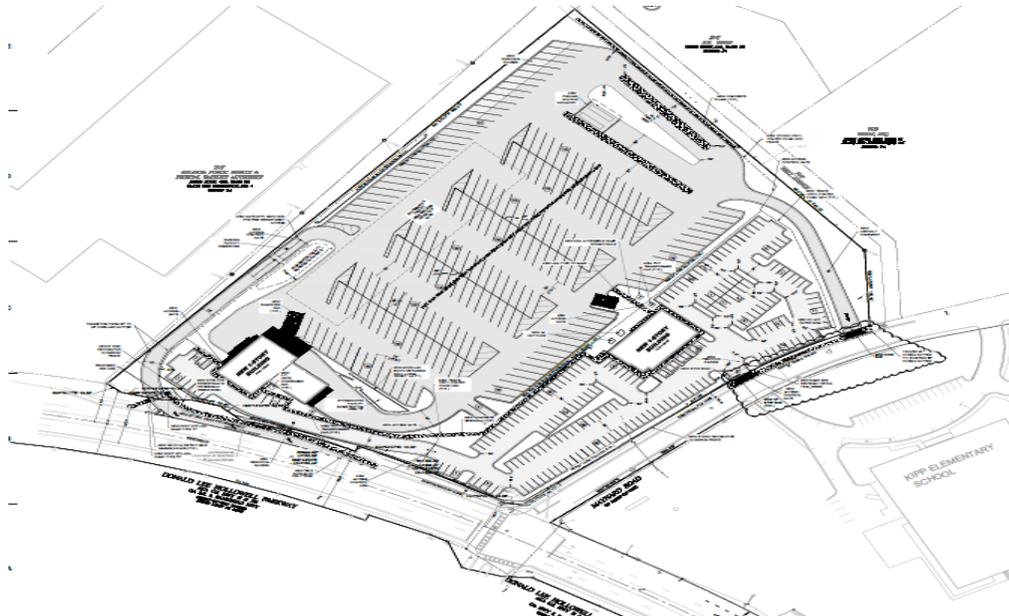

Construction Activities this week

- GDOT PERMITTING ONGOING.
- GPR (GROUND PENETRATING RADAR) UTILITY LOCATES WILL BE SCHEDULED WEEK OF (05/13/24).
- SITE INFRASTRUCTURE CONSTRUCTION (I.E., FINAL GRADING, UNDERGROUND ELECTRICAL, ETC...)
- SITE CONCRETE / CURB & GUTTER/ FLAT WORK ONGOING...
- OPERATIONS INTERIOR/EXTERIOR WALL FRAMING ONGOING. DRYWALL INSTALLATION COORDINATION ONGOING.
- MEP ROUGH-IN'S AT OPERATIONS BUILDING IS ROUGHLY 80% COMPLETED.
- MEP ROUGH IN'S ARE STARTING AT THE MAINTENANCE BUILDING.
- GA POWER POLES HAVE BEEN PLACED ONSITE. SERVICES TRANSFERRING ONGOING.
- FENCING INSTALLATION ONGOING.
- TREE/LANDSCAPING SCOPE SCHEDULED TO START. IRRIGATION SITEWORK IS ONGOING.
- ASPHALT BASE HAS STARTED.
- MASONRY MOBILIZATION IS IN COORDINATION FOR THE FOLLOWING WEEK.

CONSTRUCTION ACTIVITIES PLANNED (5 WEEK LOOK AHEAD)

THIS IS DEPENDENT UPON PERMITTING STATUS AND WEATHER.

- CURB/GUTTER/CONCRETE FLAT WORK (I.E. SIDEWALKS/DUMPSTER PADS) SCHEDULE COORDINATION IS ONGOING
- SITE CONSTRUCTION (I.E. IRRIGATION/LAND SCAPING/ LIGHT POLE)
- CIVIL CONSTRUCTION IS ONGOING.
- GA POWER COORDINATION & SERVICE IS ONGOING.
- ROW (RIGHT OF WAY) CONSTRUCTION BEING SCHEDULED.
- PERMEABLE PAVERS ARE BEING COORDINATED.
- ASPHALT WILL BE ONGOING.
- BIORETENTION SCOPE OF WORK IS BEING COORDINATED.
- REMAINING SITE DEMOLITION (MINOR AREAS THAT ARE ASSOCIATED WITH ROW/GDOT) ARE ONGOING
- FUELING STATION COORDINATION ONGOING.
- MAINTENANCE / OPERATIONS BUILDING CONSTRUCTION ONGOING.

WEEKLY CONSTRUCTION PROGRESS REPORT



MANPOWER LOG (WEEK OF 05/10/24)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	6	6	6	6	6
PENCO ELECTRICAL	4	4	4	4	4
TEBARCO MECHANICAL	4	4	4	4	4
NOVA ENGINEERING	1	1	1	1	1
VISIONSCAPES	2	2	2	2	2
JAMISON CONSTRUCTION	6	6	6	6	6
FORTRESS WALLS & HARDSCAPES	1	1	1	1	1
GEA	6	6	6	6	6
BRAVO FENCING	3	3	3	3	3
STRICTLY MECHANICAL	6	6	6	6	6
THE PAINT DOCTOR	2	2	2	2	2
BIBLER MASONRY CONTRACTOR INC.	1	1	1	1	1
MAGNUM PAVING	4	4	4	4	4

WEATHER LOG (MONTH OF DECEMBER/JANUARY/FEBRUARY/MARCH/APRIL/MAY)

- UP TO DATE, APS NW TRANSPORTATION CENTER HAS HAD (49) FORTY-NINE TRACKED RAIN DAYS IN DECEMBER/JANUARY/FEBRUARY/MARCH/APRIL/MAY.
- DAYS LOGGED: (12-01-23) / (12-02-23) / (12-03-23) / (12-08-23) / (12-09-23) / (12-10-23) / (12-24-23) / (12-25-23) / (12-26-23) / (01/06/24) / (01/08/24) / (01/09/24) / (01/12/24) / (01/16/24) / (01/19/24) / (01/24/24) / (01/25/24) / (01/26/24) / (01/27/24) / (01/28/24) / (01/29/24) / (02/04/24) / (02/10/24) / (02/11/24) / (02/12/24) / (02/22/24) / (02/28/24) / (03/01/24) / (03/04/24) / (03/05/24) / (03/06/24) / (03/08/24) / (03/10/24) / (03/15/24) / (03/22/24) / (03/26/24) / (04/02/24) / (04/08/24) / (04/09/24) / (04/10/24) / (04/11/24) / (04/17/24) / (04/19/24) / (04/20/24) / (04/21/24) / (04/30/24) / (05/04/24) / (05/05/24) / (05/09/24)
- TRACKED INCLEMENT CONDITIONS DAYS: 62 DAYS

WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT

