


# WEEKLY CONSTRUCTION PROGRESS REPORT

## Project name: Northwest Bus Transit Center

WEEK ENDING 05/31/2024

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	08/09/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

### PROJECT OVERVIEW

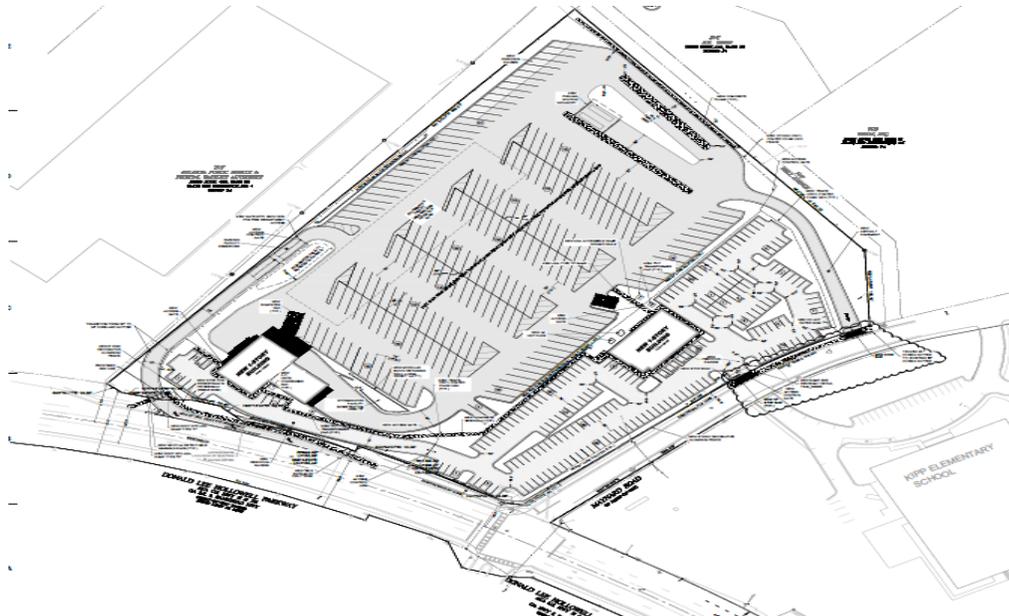

### Construction Activities this week

- GDOT PERMITTING ONGOING.
- SITE INFRASTRUCTURE CONSTRUCTION (I.E., FINAL GRADING, UNDERGROUND ELECTRICAL, ETC...)
- SITE CONCRETE / CURB & GUTTER/ FLAT WORK ONGOING...
- OPERATIONS INTERIOR/EXTERIOR WALL FRAMING 90%. MAINTENANCE ONGOING. IN WALL INSPECTION PASSED AT OPS BUILDING. APPROVED TO DRYWALL 100% IN OPS BUILDING.
- MASONRY SCOPE OF IS ONGOING AT MAINTENANCE BUILDING.
- MEP ROUGH IN'S ARE ONGOING AT THE MAINTENANCE BUILDING.
- GA POWER POLES HAVE BEEN PLACED ONSITE. SERVICES TRANSFERRING ONGOING.
- FENCING INSTALLATION ONGOING. PLEASE NOTE THAT FENCING IS BEING INSTALLED AS AREAS ARE TURNED OVER.
- TREE/LANDSCAPING SCOPE IS ONGOING AND ARE BEING INSTALLED AS AREAS ARE READY. IRRIGATION SITEWORK IS ONGOING.
- ASPHALT BASE IS ONGOING.
- FIRE SUPPRESSION (SPRINKLER SYSTEM) INSTALLATION ONGOING AT MAINTENANCE/OPS BUILDING.

### CONSTRUCTION ACTIVITIES PLANNED (LOOK AHEAD)

#### **THIS IS DEPENDENT UPON PERMITTING STATUS AND WEATHER.**

- CURB/GUTTER/CONCRETE FLAT WORK (I.E. SIDEWALKS/DUMPSTER PADS) SCHEDULE COORDINATION IS ONGOING
- MOBILIZATION OF PERMEABLE PAVERS IN COORDINATION.
- SITE CONSTRUCTION (I.E. IRRIGATION/LAND SCAPING/ LIGHT POLE)
- CIVIL CONSTRUCTION IS ONGOING.
- GA POWER/ AT&T COORDINATION & SERVICE IS ONGOING.
- SITE UTILITIES COORDINATION ONGOING.
- ROW (RIGHT OF WAY) CONSTRUCTION MOBILIZATION IS IN THE PROCESS OF BEING COORDINATED.
- ASPHALT WILL BE ONGOING.
- BIORETENTION SCOPE OF WORK IS BEING COORDINATED.
- REMAINING SITE DEMOLITION (MINOR AREAS THAT ARE ASSOCIATED WITH ROW/GDOT) ARE ONGOING
- FUELING STATION COORDINATION ONGOING.
- MAINTENANCE / OPERATIONS BUILDING CONSTRUCTION ONGOING.
- OPERATIONS BUILDING FINISHED BEING COORDINATED (I.E., TILES, PAINT, DFH, MEP FINAL TRIM)

# WEEKLY CONSTRUCTION PROGRESS REPORT




## MANPOWER LOG (WEEK OF 05/31/24)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	6	6	6	6	6
PENCO ELECTRICAL	4	4	4	4	4
TEBARCO MECHANICAL	4	4	4	4	4
NOVA ENGINEERING	1	1	1	1	1
VISIONSCAPES	6	6	6	6	6
JAMISON CONSTRUCTION	6	6	6	6	6
FORTRESS WALLS & HARDSCAPES	1	1	1	1	1
GEA	6	6	6	6	6
BRAVO FENCING	3	3	3	3	3
STRICTLY MECHANICAL	6	6	6	6	6
THE PAINT DOCTOR	1	1	1	1	1
BIBLER MASONRY CONTRACTOR INC.	7	7	7	7	7
MAGNUM PAVING	4	4	4	4	4
ALL PRO IRRIGATION	4	4	4	4	4
CENTURY FIRE PROTECTION	3	3	3	3	3
FLOR WORX	3	3	3	3	3

**WEATHER LOG (MONTH OF DECEMBER/JANUARY/FEBRUARY/MARCH/APRIL/MAY)**

- UP TO DATE, APS NW TRANSPORTATION CENTER HAS HAD (55) FIFTY-FIVE TRACKED RAIN DAYS IN DECEMBER/JANUARY/FEBRUARY/MARCH/APRIL/MAY.
- DAYS LOGGED: (12-01-23) / (12-02-23) / (12-03-23) / (12-08-23) / (12-09-23) / (12-10-23) / (12-24-23) / (12-25-23) / (12-26-23) / (01/06/24) / (01/08/24) / (01/09/24) / (01/12/24) / (01/16/24) / (01/19/24) / (01/24/24) / (01/25/24) / (01/26/24) / (01/27/24) / (01/28/24) / (01/29/24) / (02/04/24) / (02/10/24) / (02/11/24) / (02/12/24) / (02/22/24) / (02/28/24) / (03/01/24) / (03/04/24) / (03/05/24) / (03/06/24) / (03/08/24) / (03/10/24) / (03/15/24) / (03/22/24) / (03/26/24) / (04/02/24) / (04/08/24) / (04/09/24) / (04/10/24) / (04/11/24) / (04/17/24) / (04/19/24) / (04/20/24) / (04/21/24) / (04/30/24) / (05/04/24) / (05/05/24) / (05/09/24) / (05/13/24) / (05/14/24) / (05/17/24) / (05/18/24) / (05/24/24) / (05/27/24)
- TRACKED INCLEMENT CONDITIONS DAYS: 68 DAYS

WEEKLY CONSTRUCTION PROGRESS REPORT

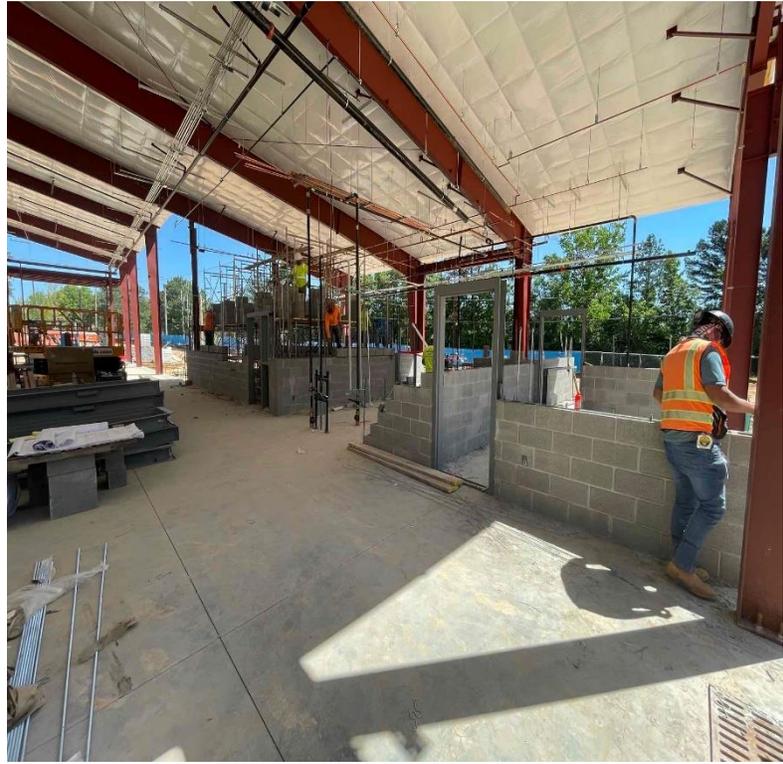

WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT

