


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit center

WEEK ENDING 12/01/2023

Initial information	Data
PROJECT BUDGET (GMP)	\$19,664,171.00
START DATE	09/19/2023
COMPLETION DATE	07/31/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

PROJECT OVERVIEW

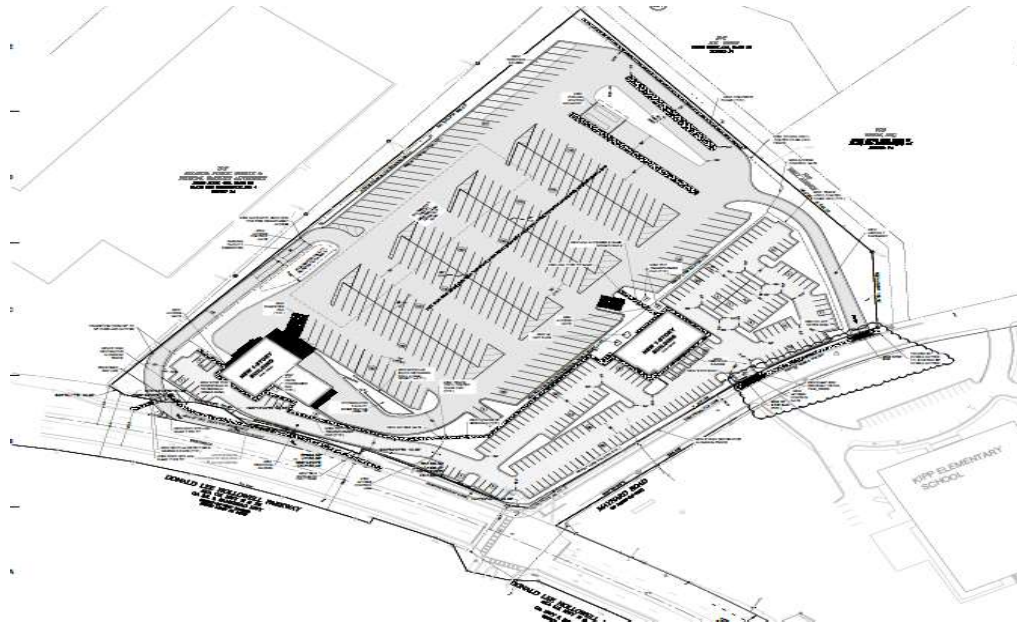

WEEKLY CONSTRUCTION PROGRESS REPORT



Construction Activities this week

- IN THE PROCESS OF CONDUCTING CIVIL WORK
- MASS GRADING THE SITE
- LAYDOWN AREA PREP
- BUILDING PAD PREP
- BIORETENTION PREP
- INSTALLING STORM STRUCTURES
- COORDINATING A LOGISTICS PLAN FOR SS BORE ACROSS MAYNARD STREET
- EXCAVATING THE RETENTION BASIN.

CONSTRUCTION ACTIVITIES PLANNED (5 WEEK LOOK AHEAD)



THIS IS DEPENDENT UPON BUILDING PERMIT STATUS AND WEATHER.

- CONCRETE, REBAR, PLUMBING & ELECTRICAL EQUIPMENT DELIVERIES
- STRUCTURAL FOUNDATION LAYOUT
- CONTINUE TO WORK ON BUILDING PADS
- UNDERSLAB PLUMBING INSTALLATION (MEP INSTALLATION)
- CONCRETE WORK/POUR SLABS

MANPOWER LOG (WEEK OF 12/01/23)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	25	25	25	25	0

WEEKLY CONSTRUCTION PROGRESS REPORT

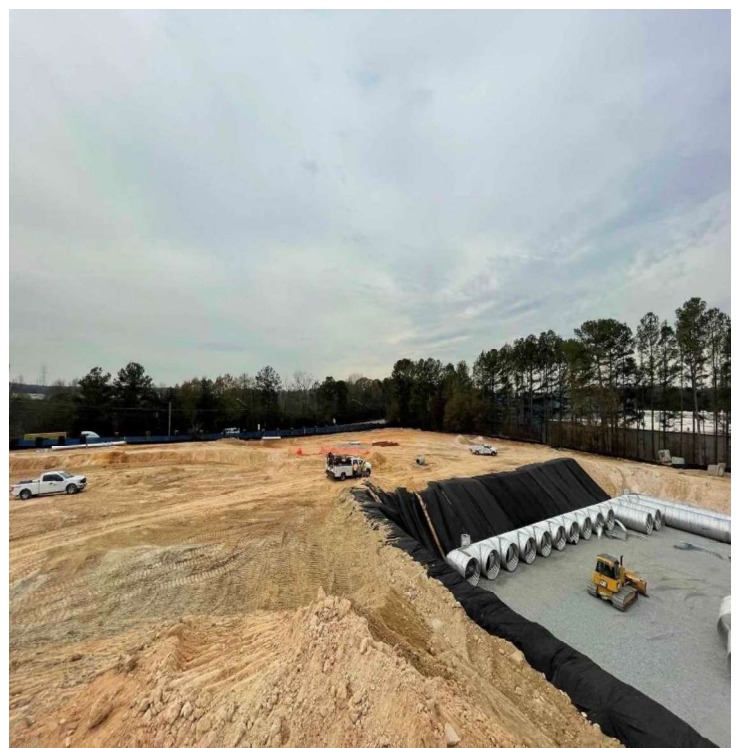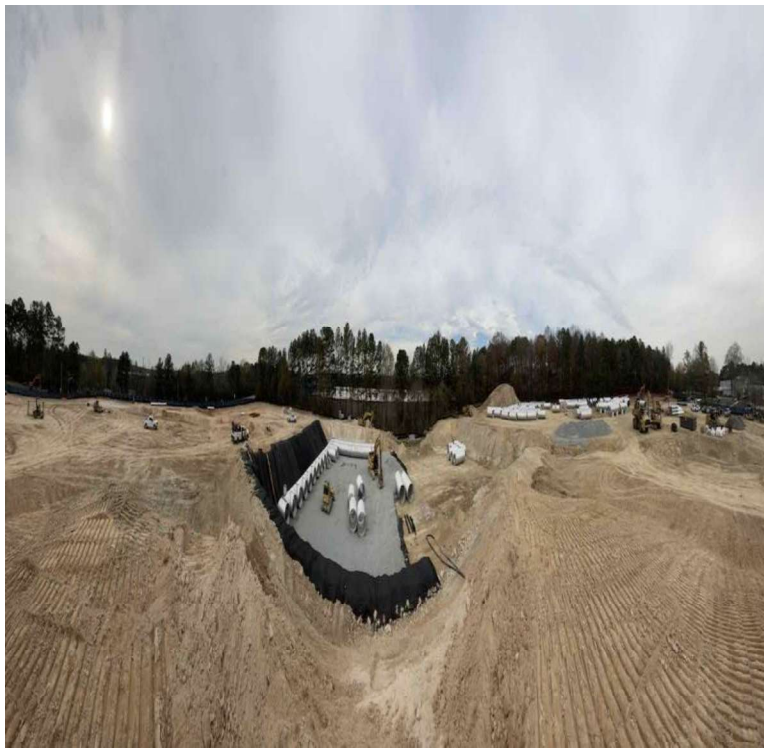

WEEKLY CONSTRUCTION PROGRESS REPORT

