


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit Center

WEEK ENDING 06/21/2024

Initial information	Data
PROJECT BUDGET (GMP)	\$20,644,215.00
START DATE	09/19/2023
COMPLETION DATE	10/15/2024
NAME OF THE CMAR	AJAX BUILDING COMPANY
PROJECT MANAGER FROM CMAR	LAMONT EAKINS
PROJECT MANAGER FROM APS	ALEX REVIN
PREPARED BY	SHYHEIM HOWARD

PROJECT OVERVIEW

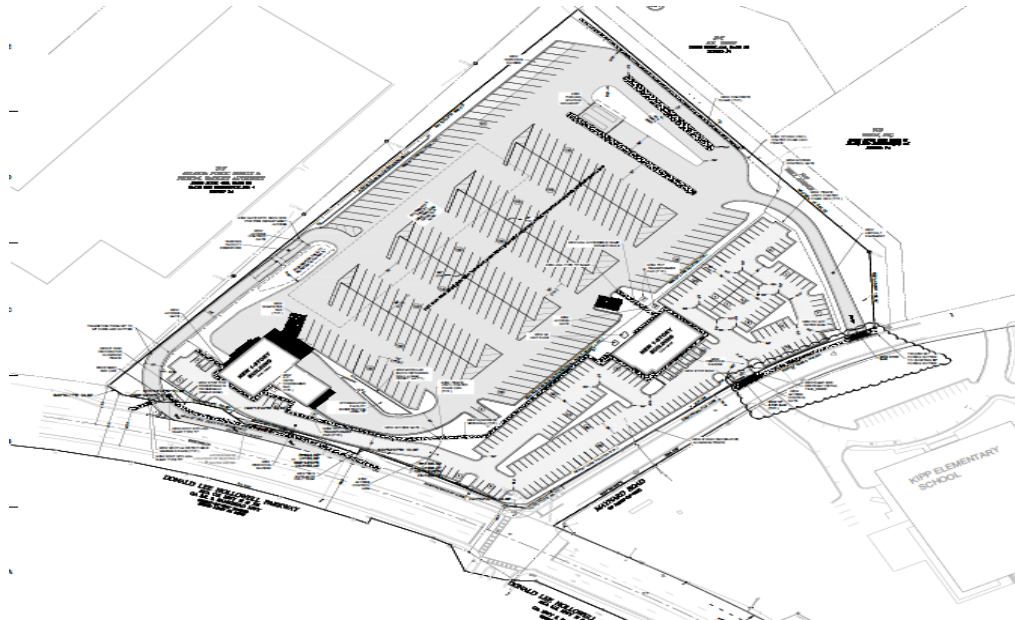

Construction Activities this week

- GDOT/GUPS PERMITTING ONGOING.
- SITE INFRASTRUCTURE CONSTRUCTION (I.E., FINAL GRADING, UNDERGROUND ELECTRICAL, ETC...)
- SITE CONCRETE / CURB & GUTTER/ FLAT WORK ONGOING...
- OPERATIONS INTERIOR ONGOING. DRYWALL COMPLETION 95%.
- OPERATION BUILDING EXTERIOR WALL FRAMING 90%.
- MAINTENANCE BUILDING MASONRY CONSTRUCTION 85%.
- MEP ROUGH IN'S AT THE MAINTENANCE BUILDING 85% COMPLETED.
- FENCING INSTALLATION ONGOING. PLEASE NOTE THAT FENCING IS BEING INSTALLED AS AREAS ARE TURNED OVER.
- TREE/LANDSCAPING SCOPE IS ONGOING AND ARE BEING INSTALLED AS AREAS ARE READY. IRRIGATION SITEWORK IS ONGOING.
- ASPHALT BASE IS 70% COMPLETED. REMAINING WORK IS ONGOING.
- FIRE SUPPRESSION (SPRINKLER SYSTEM) INSTALLATION ONGOING AT MAINTENANCE/OPS BUILDING IS ONGOING.
- GLASS & GLAZING SCOPE AT OPERATIONS BUILDING IS 85% COMPLETED.
- GLASS & GLAZING SCOPE AT MAINTENANCE BUILDING STAGED TO COMMENCE IN UP COMING WEEKS.
- ROW (RIGHT OF WAY) WORK HAS MOBILIZED.
- GA POWER HAS ENERGIZED TEMPORARY POWER AT BOTH BUILDINGS AND REMOVED TENSION POLE ONSITE.

CONSTRUCTION ACTIVITIES PLANNED (LOOK AHEAD)

THIS IS DEPENDENT UPON PERMITTING STATUS AND WEATHER.

- CURB/GUTTER/CONCRETE FLAT WORK (I.E. SIDEWALKS/DUMPSTER PADS) SCHEDULE COORDINATION IS ONGOING
- MOBILIZATION OF PERMEABLE PAVERS IN COORDINATION.
- SITE CONSTRUCTION (I.E. IRRIGATION/LAND SCAPING/ LIGHT POLE) IS ONGOING.
- CIVIL CONSTRUCTION IS ONGOING.
- GA POWER/ AT&T COORDINATION & SERVICE IS ONGOING.
- SITE UTILITIES COORDINATION ONGOING.
- ROW (RIGHT OF WAY) CONSTRUCTION MOBILIZATION IS IN THE PROCESS OF BEING COORDINATED.
- ASPHALT WILL BE ONGOING.
- BIORETENTION SCOPE OF WORK IS BEING COORDINATED.
- REMAINING SITE DEMOLITION (MINOR AREAS THAT ARE ASSOCIATED WITH ROW/GDOT) ARE ONGOING
- FUELING STATION COORDINATION ONGOING.
- MAINTENANCE / OPERATIONS BUILDING CONSTRUCTION ONGOING.
- OPERATIONS BUILDING FINISHED BEING COORDINATED (I.E., TILES, PAINT, DFH, MEP FINAL TRIM)

WEEKLY CONSTRUCTION PROGRESS REPORT




MANPOWER LOG (WEEK OF 06/21/24)

SUBCONTRACTOR	M	T	W	TH	F
LEWIS CONTRACTING	8	8	8	8	8
PENCO ELECTRICAL	6	6	6	6	6
TEBARCO MECHANICAL	4	4	4	4	4
NOVA ENGINEERING	1	1	1	1	1
VISIONSCAPES	6	6	6	6	6
D & D GLASS	2	2	2	2	2
GEA	6	6	6	6	6
STRICTLY MECHANICAL	4	4	4	4	4
BIBLER MASONRY	7	7	7	7	7
PAINT DOCTOR	2	2	2	2	2
CENTURY FIRE	3	3	3	3	3
FLOOR WORX	5	5	5	5	5
JAMISON	6	6	6	6	6


WEATHER LOG (MONTH OF DECEMBER/JANUARY/FEBRUARY/MARCH/APRIL/MAY/JUNE)

- UP TO DATE, APS NW TRANSPORTATION CENTER HAS HAD (57) FIFTY-SEVEN TRACKED RAIN DAYS IN DECEMBER/JANUARY/FEBRUARY/MARCH/APRIL/MAY/JUNE.
- DAYS LOGGED: (12-01-23) / (12-02-23) / (12-03-23) / (12-08-23) / (12-09-23) / (12-10-23) / (12-24-23) / (12-25-23) / (12-26-23) / (01/06/24) / (01/08/24) / (01/09/24) / (01/12/24) / (01/16/24) / (01/19/24) / (01/24/24) / (01/25/24) / (01/26/24) / (01/27/24) / (01/28/24) / (01/29/24) / (02/04/24) / (02/10/24) / (02/11/24) / (02/12/24) / (02/22/24) / (02/28/24) / (03/01/24) / (03/04/24) / (03/05/24) / (03/06/24) / (03/08/24) / (03/10/24) / (03/15/24) / (03/22/24) / (03/26/24) / (04/02/24) / (04/08/24) / (04/09/24) / (04/10/24) / (04/11/24) / (04/17/24) / (04/19/24) / (04/20/24) / (04/21/24) / (04/30/24) / (05/04/24) / (05/05/24) / (05/09/24) / (05/13/24) / (05/14/24) / (05/17/24) / (05/18/24) / (05/24/24) / (05/27/24) / (06/04/24) / (06/06/24)
- TRACKED INCLEMENT CONDITIONS DAYS: 70 DAYS

WEEKLY CONSTRUCTION PROGRESS REPORT

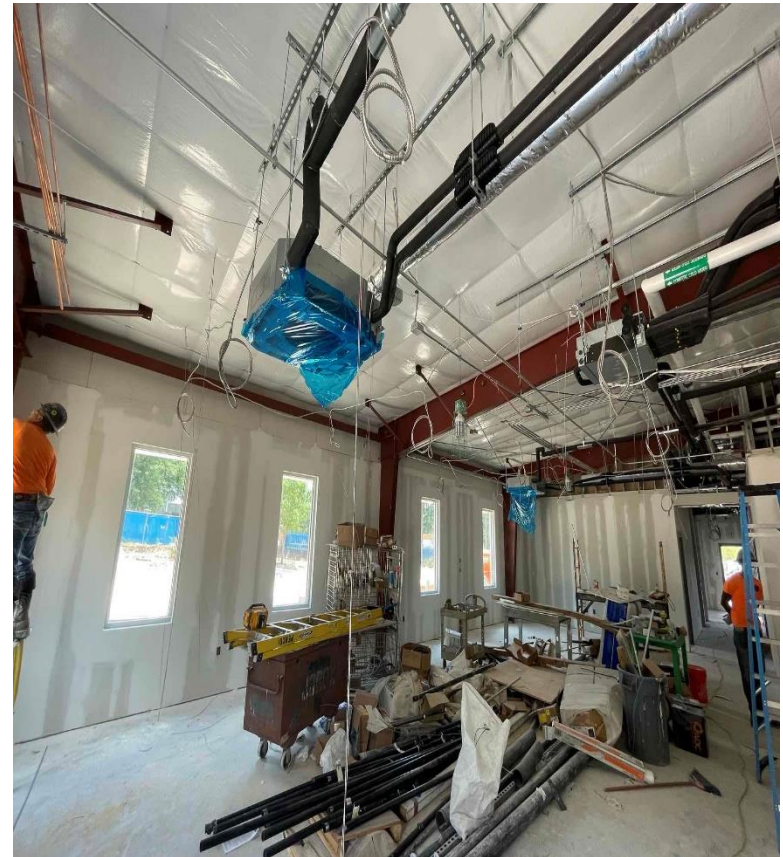

WEEKLY CONSTRUCTION PROGRESS REPORT

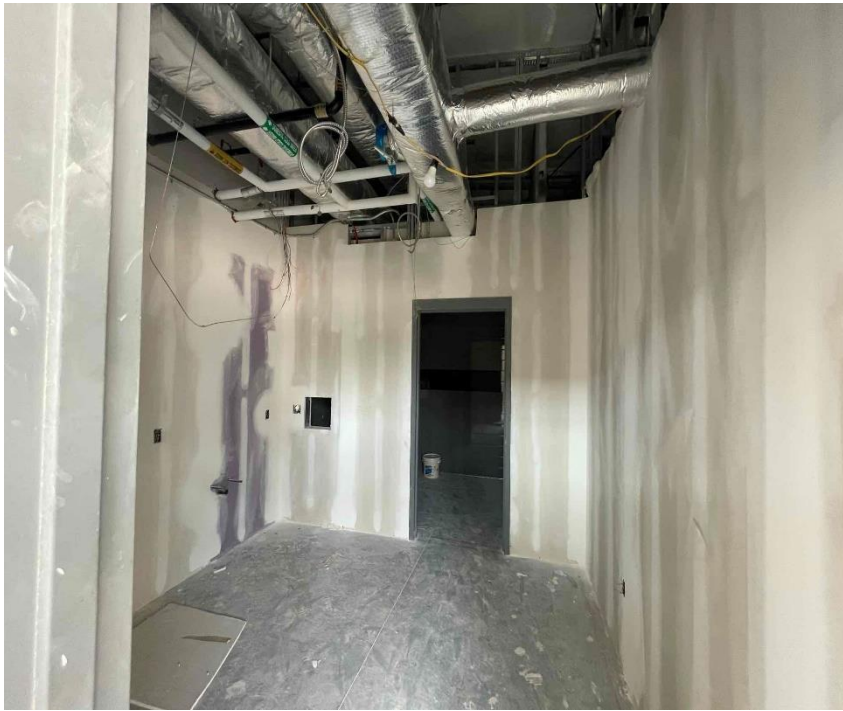

WEEKLY CONSTRUCTION PROGRESS REPORT

