


WEEKLY CONSTRUCTION PROGRESS REPORT

Project name: Northwest Bus Transit center

WEEK ENDING 10/13/2023

| Initial information | Data |
|---------------------------|-----------------------|
| PROJECT BUDGET (GMP) | \$19,664,171.00 |
| START DATE | 09/19/2023 |
| COMPLETION DATE | 07/31/2024 |
| NAME OF THE CMAR | AJAX BUILDING COMPANY |
| PROJECT MANAGER FROM CMAR | LAMONT EAKINS |
| PROJECT MANAGER FROM APS | ALEX REVIN |
| PREPARED BY | LAMONT EAKINS |

PROJECT OVERVIEW

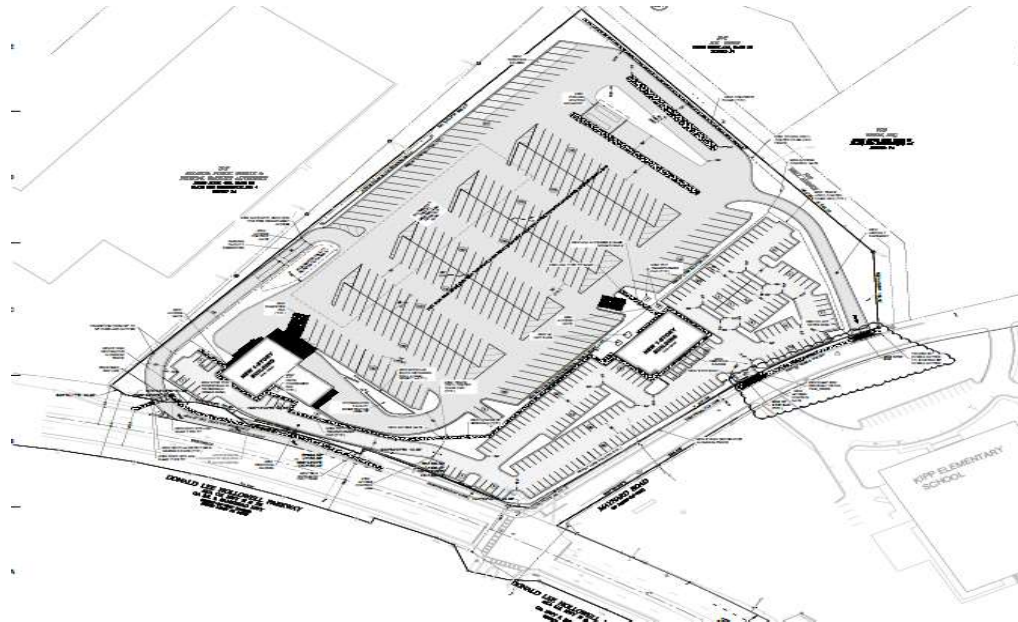

Construction Activities this week

- CLEARING/GRUBBING AND DEFORESTATION OF THE PROJECT JOBSITE
- MEP & UTILITY COORDINATION

CONSTRUCTION ACTIVITIES PLANNED NEXT WEEK

- CONTINUE WITH SITE CLEARING AND GRUBBING
- MOBILIZING STRUCTURES AND START CONSTRUCTION OF SITE
- FINISH SETTING JOBSITE TRAILER (POWER, INTERNET, ETC.)

WEEKLY CONSTRUCTION PROGRESS REPORT



WEEKLY CONSTRUCTION PROGRESS REPORT

