


*Quote of the week: "When i let go of what i am , i become what i might be."*

## Project: FL Stanton ES Renovation and Addition

**Week ending: April 19, 2024**

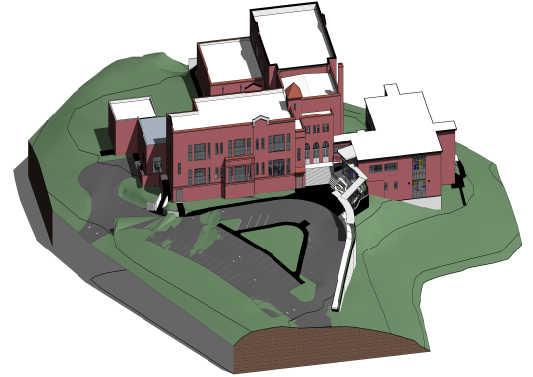

- Wood doors delivered
- Installed storefront glass and windows
- All plaster repairs are complete
- Installed helical piers
- Complete gymnasium drywall finishing
- framed ramp and stair at gym stage
- Framed media center walls
- Begin gas line on the roof



*Continue with storefront glass install*



*Complete column footing pour back  
for security vestibule*



*Backfill at the retaining wall is complete*



*Continue installing all HVAC duct and continue metal stud framing*

## **NEXT WEEK – April 22 - April 26**

- Complete VRF piping and drains
- Begin security vestibule footings and slab pour back
- Begin resinous flooring work at all bathroom/kitchen
- Install headwall/junction box at underground detention pond
- Begin brick cleaning and pressure washing
- Demo duct banks for completion of storm water and sanitary sewer
- Distribution panels are set to be delivered

## **SCHEDULED DATE OF SUBSTANTIAL COMPLETION**

- June 30 , 2024

## **Final Completion**

- June 30, 2024

## **PREPARED BY:**

Jahaziel Lee, Carroll Daniel Construction Co.
