


Quote of the week: "Don't wait for the right time. Create it."

Project: Toomer ES Additions and Modifications

Week Ending: September 15, 2023

THIS WEEK:

- Completed demo in area 3 on the first floor
- All Precast double tees have been removed
- Completed underground plumbing in area 2
- Continued MEP overhead rough in area 3
- Completed saw-cuts and slab removal for underground plumbing in area 3
- Begin fire sprinkler system installation
- Stucco wall demo is completed
- Begin installing structural shoring in area 2
- Begin installing overflow drains

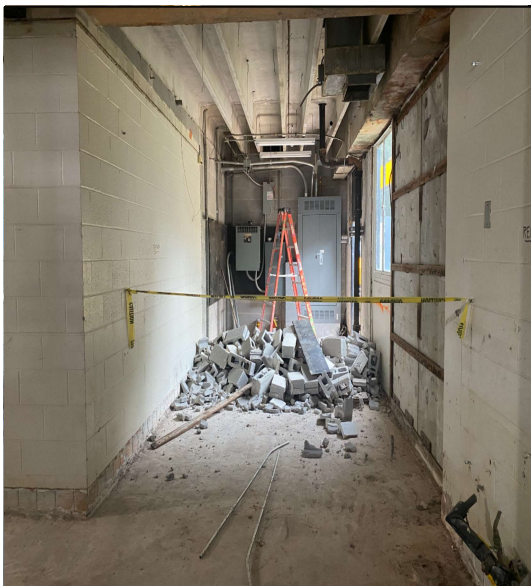

Continue demo throughout



*Structural shoring has begun in area
2*




Began installing erosion control silk fence



Continue installing duct in the cafeteria.



Began installing racks in the kitchen area

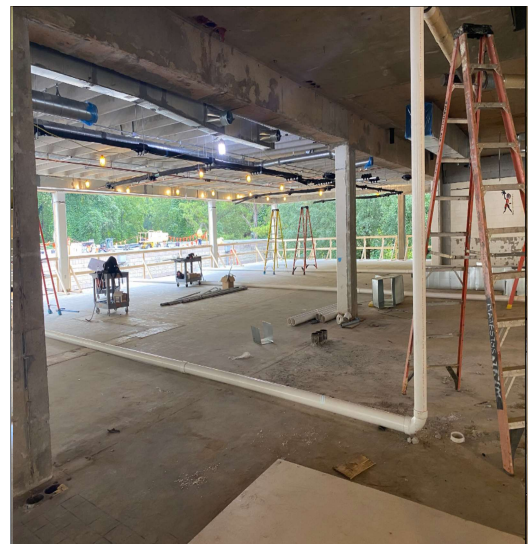

Begin replacing roof drain piping

NEXT WEEK – September 18 - September 22

- Begin installing roof curbs and support steel in area 2
- Start TPO roofing in area 2
- Cut penetrations in concrete roof deck area 3
- Demo load bearing walls in area 2
- Continue overhead MEP rough in areas 2 and 3
- Radar scan poured in place concrete roof deck and second floor slab at new penetration areas
- Excavate and pour column footings in area 2
- Install structural steel in area 2

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- June 30, 2024

Final Completion

- June 30, 2024

PREPARED BY:

Jahaziel Lee, Carroll Daniel Construction Co.
