


Quote of the week: " Today has something we will need for tomorrow. Lets go find what it is."

## Project: Toomer ES Additions and Modification


Week Ending: March 22, 2024

### THIS WEEK:

- Continue installing devices in areas 1 and 2
- Continue installing lights in the area 1, lobby.
- Continue Fire alarm system install
- Install lighting at rear aluminum canopy
- Continue pulling the control wires in areas 1 and 2
- Complete condensate hookups to VRF units
- Pulling vacuums on various VRF systems
- Install water heater in area 2
- Continue dropping sprinkler heads in area 1 and 2
- Complete Ceiling grid install in the security vestibule and lobby area




Begin installing plumbing fixtures

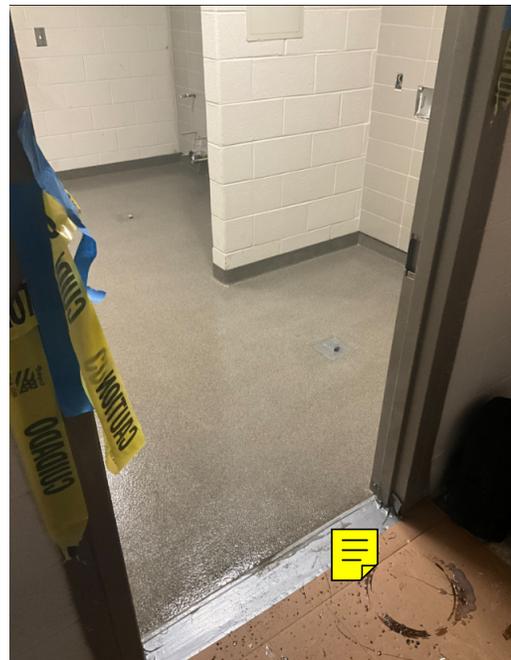

Area 3 , second floor bathroom epoxy floors are complete



*Ceiling grid install is 90% Complete throughout.*

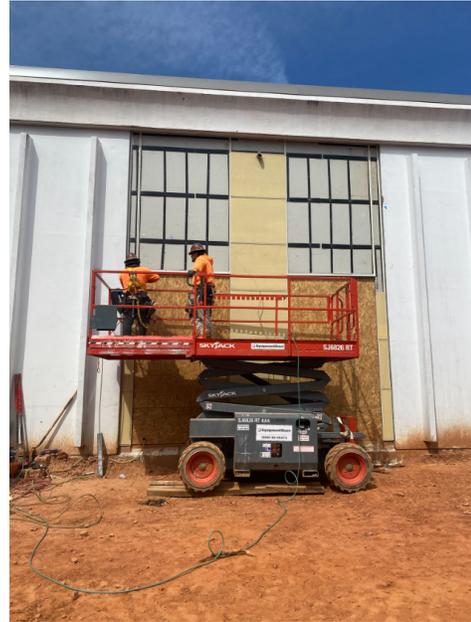

*Continue to install FCP*

## **NEXT WEEK – March 25 - March 29**

- Complete ceramic tile install in area 1
- Begin infiltration pond and associated storm pipe
- Begin laying CMU block at the monument sign
- Complete area 3 final paint
- Continue pulling low voltage wire in area 1
- Complete fixture install in all bathrooms

## **SCHEDULED DATE OF SUBSTANTIAL COMPLETION**

- June 30, 2024

## **Final Completion**

- June 30, 2024

## **PREPARED BY:**

Jahaziel Lee, Carroll Daniel Construction Co.
