


Quote of the week: "Your dreams are worth it. Persevere. Your focus is your power. Harness it. ."

Project: Toomer ES Additions and Modification


Week Ending: April 19, 2024

THIS WEEK:

- Electrician is working on getting lighting and power circuits on line
- Continue install fire alarm devices and testing
- Continue working on intercom system install
- Begin rerouting power to the gym
- RTU and Doas Start up begin Monday
- Continue installing Classroom sinks
- Complete fixture install in the gym
- Continue with drinking fountain rework



Begin installing canopies at the security vestibule

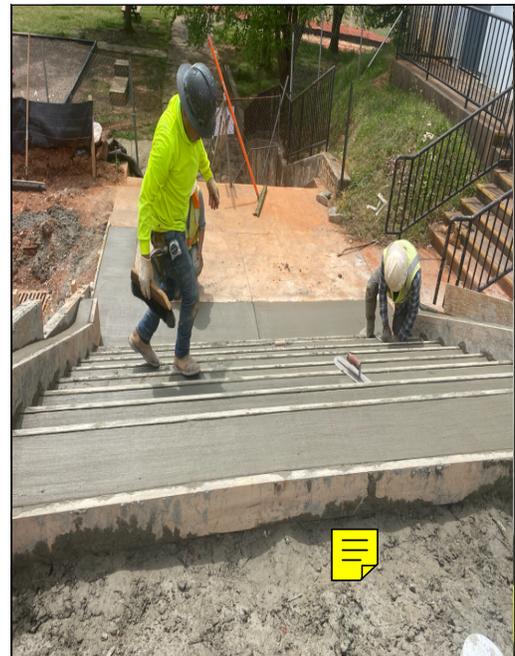

Begin forming and pouring back stairs at the gym and security vestibule



Begin curb and gutter construction for the dumpster pad



Begin metal stud framing for fire riser in the flex room

NEXT WEEK – April 22 - April 26

- Continue connecting gym supply piping
- Continue fire sprinkler testing
- Continue with concrete paving and curb & gutter
- Begin forming sidewalks
- Continue with VCT install in area 1 and 2
- Continue with exterior paint
- Begin VRF start- up

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- June 30, 2024

Final Completion

- June 30, 2024

PREPARED BY:

Jahaziel Lee, Carroll Daniel Construction Co.
