


*Quote of the week: "Your dreams are worth it. Persevere. Your focus is your power. Harness it. ."*

## Project: Toomer ES Additions and Modification


**Week Ending: April 19, 2024**

### THIS WEEK:

- Electrician is working on getting lighting and power circuits on line
- Continue install fire alarm devices and testing
- Continue working on intercom system install
- Begin rerouting power to the gym
- RTU and Doas Start up begin Monday
- Continue installing Classroom sinks
- Complete fixture install in the gym
- Continue with drinking fountain rework



*Begin installing canopies at the security vestibule*

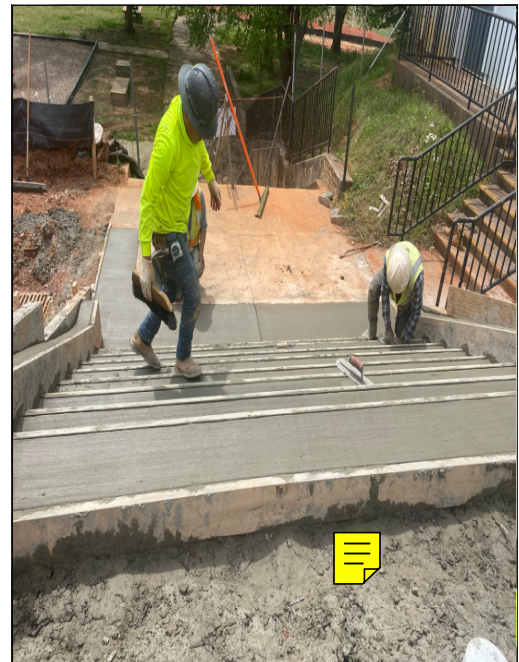

*Begin forming and pouring back stairs at the gym and security vestibule*



*Begin curb and gutter construction  
for the dumpster pad*



*Begin metal stud framing for fire  
riser in the flex room*

## **NEXT WEEK – April 22 - April 26**

- Continue connecting gym supply piping
- Continue fire sprinkler testing
- Continue with concrete paving and curb & gutter
- Begin forming sidewalks
- Continue with VCT install in area 1 and 2
- Continue with exterior paint
- Begin VRF start- up

## **SCHEDULED DATE OF SUBSTANTIAL COMPLETION**

- June 30, 2024

## **Final Completion**

- June 30, 2024

## **PREPARED BY:**

Jahaziel Lee, Carroll Daniel Construction Co.
