


*Quote of the week: "Learn from yesterday, live for today, hope for Tomorrow."*

## Project: Toomer ES Additions and Modification


**Week Ending: October 20, 2023**

### THIS WEEK:

- Continue working on installing new TPO roofing in area 3
- Metal stud framing in area 3 in complete
- Plumbing underground in the kitchen is complete
- Continue overhead MEP rough areas in 1,2 and 3
- Began prepping for pour back of concrete trenches in the kitchen and topping slab
- Underground Plumbing Inspection
- Continue underground plumbing rough in the corridor area.
- Began installing hollow metal frames in existing openings in area 2
- Began infilling CMU block in area 2
- In wall plumbing inspections is complete
- Began installing cassettes and branch selectors




*Continue underground plumbing backfill in corridor area 3*

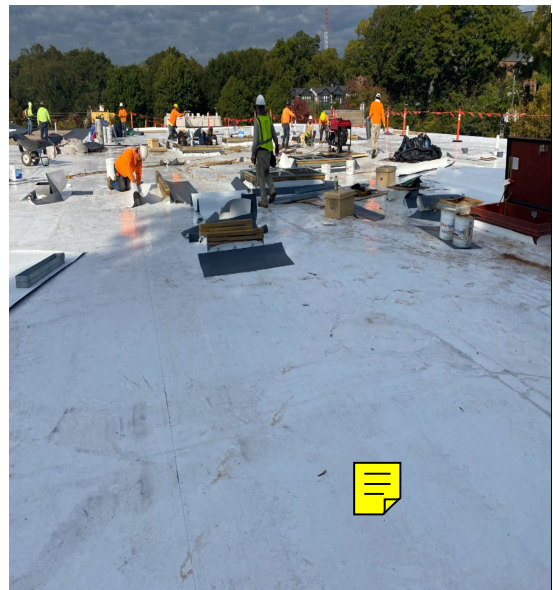

*Continue Installing new TPO roofing system*



*Continue Installing branch selectors  
in area 3 level 1*

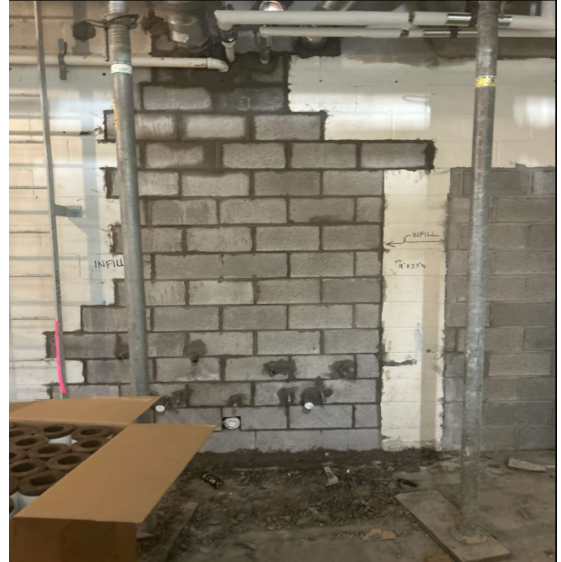

*Continue to install CMU block infill  
around all in wall plumbing in area 2*



*Continue installing conduit and  
raceway boxes throughout*



*Continue installing hollow metal  
frames in area 2*

**NEXT WEEK – October 23 - October 27**

- Begin installing roof curbs in area 2 and 3
- Began metal stud framing on the 1st floor of area 3
- Began Sheathing exterior walls in area 3
- Begin Fabrication of Structural Steel in area 2 - Monday 10.23.23
- Backfill underground plumbing in the corridor area for inspection
- Pour prep and pour back to begin in the kitchen and corridor area 3
- Continue installing conduit throughout
- In Wall Plumbing inspections

**SCHEDULED DATE OF SUBSTANTIAL COMPLETION**

- June 30, 2024

**Final Completion**

- June 30, 2024

**PREPARED BY:**

Jahaziel Lee, Carroll Daniel Construction Co.
