



*Quote of the week: "Do today what should be done."*

## Project: Toomer ES Additions and Modification

**Week Ending: September 29, 2023**

### THIS WEEK:

- Installed structural shoring in area 2
- Completed demo of all load bearing walls
- Started roof repair at areas 1,2, and 3
- Wet areas at the roof have been removed and patched back with installation and TPO
- Begin concrete roof and floor penetrations area 3
- Continued MEP overhead rough in areas 2 and 3
- Completed underground sanitary and roof drain piping in area 3
- Begin slab prep in area 3 at plumbing pour backs
- Completed trench removal and footing at area 1 except for the kitchen area
- Begin Trench pour back in area 3 and area 1
- Plumbing inspection is set for friday ,09-29-23

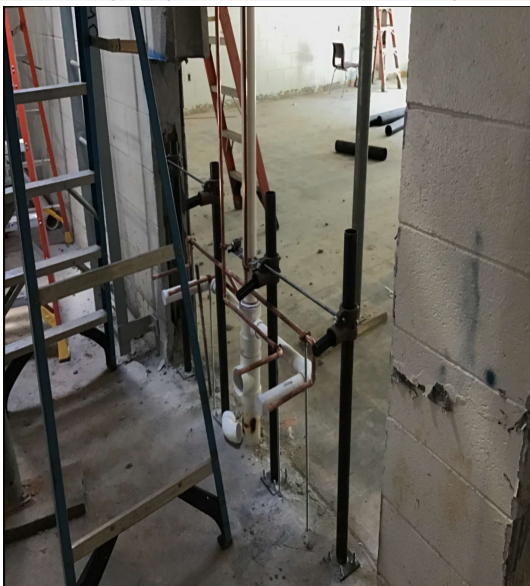

*Begin prepping all in wall rough in for new Plumbing fixtures and new CMU block*



*Begin hanging new fire sprinkler system*




*Trench pour back prep. Begin pouring back on Thursday - 09/28/23*



*Roof curb removal has begun*



*Shoring is complete in area 2*

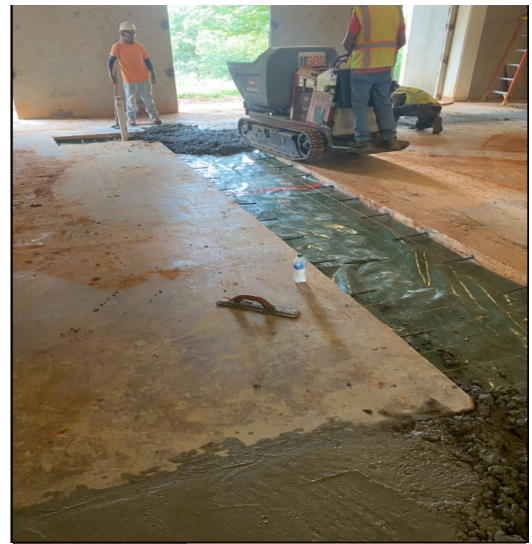

*Begin trench pour back in area 3*

**NEXT WEEK – October 2 - October 6**

- Install structural steel support framing in areas 2 and 3
- Install roof curbs in areas 2 and 3
- Begin TPO roofing area 2
- Continue pour back at area 3 and cafeteria
- Pour topping slabs in area 2
- Install plumbing underground in area 1
- Continue overhead MEP rough areas 1,2 and 3
- Begin Fabrication for structural steel in area 2
- Excavate and pour column footing in area 2

**SCHEDULED DATE OF SUBSTANTIAL COMPLETION**

- June 30, 2024

**Final Completion**

- June 30, 2024

**PREPARED BY:**

Jahaziel Lee, Carroll Daniel Construction Co.
