


Quote of the week: " Ask yourself if what you're doing today is getting you closer to where you want to be tomorrow."

Project: Toomer ES Additions and Modification


Week Ending: March 15, 2024

THIS WEEK:

- Begin FCP Installation (Mock -up)
- Permanent power inspection has passed
-
-
-
-
-
-



Continue to prep canopy footings a vestibule entry for pour back

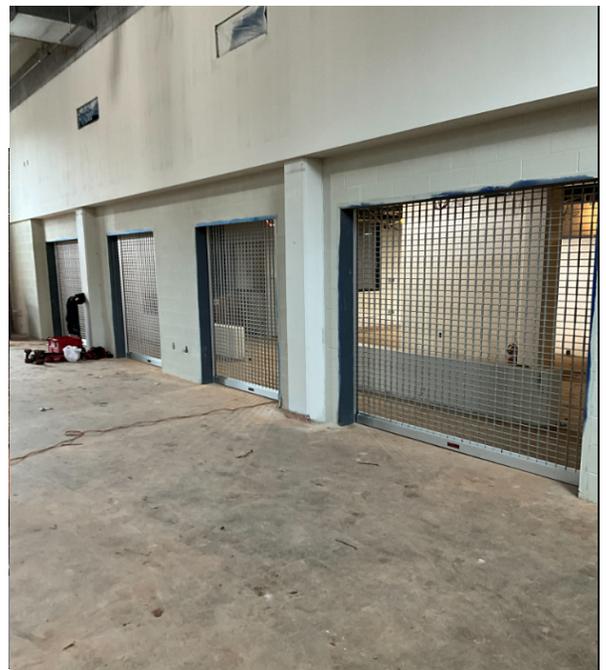

Overhead coiling doors have been installed



Installing new downspouts and coping



Complete demo for new Fire Riser

NEXT WEEK – March 11 - March 15

- Remove fixtures at the gym
- Finish drywall at lobby soffit
- Complete condensate hookups to VRF units
- Complete condensate drains on roof
- Ceiling cover up inspection for area 3 is complete
- Getting material together to run a new gas line from area 1 to the gym.

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- June 30, 2024

Final Completion

- June 30, 2024

PREPARED BY:

Jahaziel Lee, Carroll Daniel Construction Co.
