

Quote of the week: "We do not remember days. We remember moments."



Project: Toomer ES Additions and Modifications

Week Ending: September 1 ,2023


THIS WEEK:

- Continued demo area 3 first floor.
- Completed wall layout second floor area 3.
- Plumbing underground started and near completion area 2.
- Installing ductwork area 3 second floor.
- Installing plumbing overhead rough area 2.
- Saw cutting slab at area 3 for underground plumbing.
- Installing refrigerant piping hangers in area 2 and 3.
- Removing stucco exterior wall at area 3.
- Completed backfill in on level 1 area 2 today -

09/01/2023

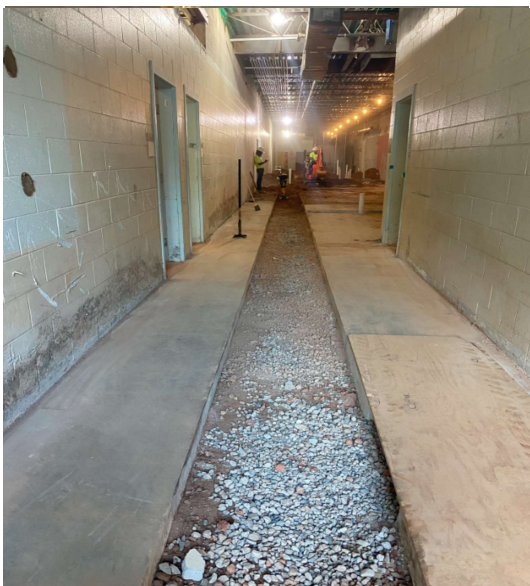

*plumbing inspection is complete
and begin trench backfill in area 2
level 1*

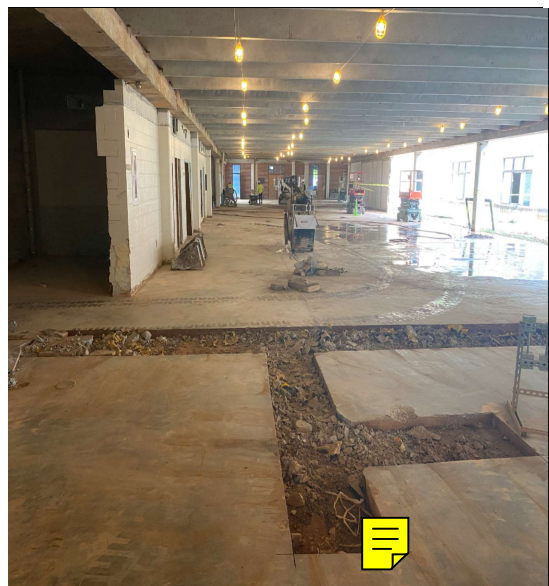


Began trench demo in area 2 level 1



Began exterior wall demo



Continue installing all new conduit, Refrigerant piping and racks as well as duct work

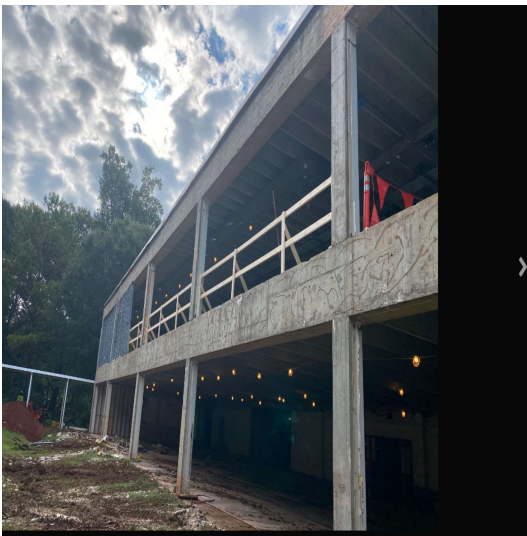

Continue to install fall protection safety rails on the second floor of area 3 level 2



Began removal of precast double T's

NEXT WEEK – September 4 - September 8

- Continue demo at kitchen- Asbestos abatement is complete
- Demo all precast double tees.
- Remove concrete slab for plumbing underground at area 3.
- Complete all demo areas 1, 2, and 3.
- Pour back concrete slab at plumbing trenches and start structure shoring at area 2.
- Continue overhead MEP rough areas 2 and 3.
- Radar scan poured in place concrete roof deck and second floor slab at new penetration areas.

SCHEDULED DATE OF SUBSTANTIAL COMPLETION

- June 30, 2024

Final Completion

- June 30, 2024

PREPARED BY:

Jahaziel Lee, Carroll Daniel Construction Co.
