

**WEEKLY CONSTRUCTION PROGRESS REPORT**  
**Construct Field Houses, S. Atlanta and Carver High Schools**  
**May 6, 2021**

Prepared For: Atlanta Public Schools

Prepared By: Michael Bower




*Figure 1 S. Atl – Exterior Soffit and Lights*



*Figure 2 S. Atl – Block Filler*



*Figure 3 Carver – Epoxy floor*

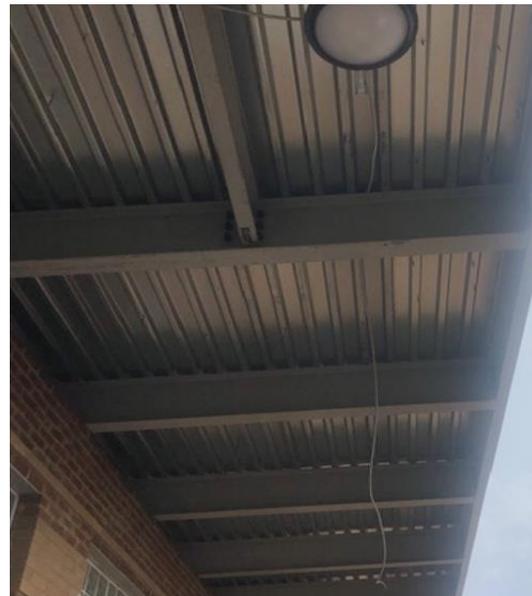

*Figure 4 Carver – Soffit Electrical Rough-In*



## WEEKLY CONSTRUCTION PROGRESS REPORT

Construct Field Houses, S. Atlanta and Carver High Schools

May 6, 2021

### Last Week's Activities:

- Carver HS – Exterior man doors and hardware, electrical and mechanical rough-in, prep and place epoxy floors.
- S. Atlanta HS – Hard ceiling framing, electrical rough-in, prep and place epoxy floors, exterior soffit.

### This Week's Activities:

- Carver HS – Exterior soffit electrical rough-in, steel field fix, cmu tooth in to underside of deck.
- S. Atlanta HS – Brick pressure wash, Mechanical and electrical rough, plumbing rough, install Flo-well and site clean-up, block fill and first coat of paint.

### Next Week's Activities:

- Carver HS – Plumbing rough-in, brick pressure wash, block fill and first coat of paint, cmu tooth in to deck, MEP rough-in, interior doors.
- S. Atlanta HS – MEP fans, finish electrical rough above ceiling and prep for ceiling closure inspection.

### Schedule:

- Revised Target Completion dates of 6/14 and 7/2 (S. Atl and Carver respectively) shows a slight expected improvement in the scheduled dated 3/5/21. The GC has shown improved manpower and progress consistently above and beyond previous efforts with Brown and Root continuing assistance with cash flow for the GC.

### Budget:

- Construction Budget:
  - Carver: \$806,230
  - S. Atlanta: \$604,946
- Budget Status: On Budget
- Gross Billed to Date:
  - Carver: \$554,192
  - S. Atlanta: \$443,337
